项目装修复核检查表

项目名称	美国高尔夫球舱高尔夫派			
项目地址	美国			
检查内容	内容细节	是否合格	实际尺寸	备注
慕布	安装幕布四周角铁位置12mm厚阻燃版伸出不小于80mm。	是口 否口		如现场情况没有超出80mm,幕布安装好四周很大缝隙，影响美观后期打球时会出现球掉入幕布后面的情况。
	幕布距离后墙距离300mm。	是口 否口		如现场情况没有300mm,后期会影响工程师在安装悬挂幕布的效率，会影响幕布的平整度。
	侧面软包面距离侧墙面100mm,软包吊顶面距离天花面100mm。	是口 否口		如现场情况没有150mm,后期会影响工程师在安装悬挂幕布的效率，会影响幕布的平整度。
	幕布顶部木板需加固，承重50KG。	是口 否口		如现场情况没有做加固处理，会造成幕布挂不上而造成慕布整体下掉。
打击台	打击台造型已完成。(打击垫尺寸：1500mm*1800mm/1200mm*1800mm)	是口 否口		此区域尺寸必须精准，如尺寸有误差会影响整个打击垫区域。
	打击垫下沉区域标高比打台低25mm;必须符合图纸尺寸要求。	是口 否口		此区域尺寸必须精准，如尺寸有误差会导致整个打击垫区域凸起或者凹陷。
缓冲坡	缓冲坡造型已完成，缓冲坡最低点必须高于预埋件入球口。	是口 否口		如回球口最低点不高于进球口会导致无法正常回球。
	尺寸符合图纸尺寸要求。	是口 否口		如不符会导致上球机无法正常使用。
回球槽	不锈钢按要求贴好，不得高于木板面。	是口 否口		如未贴不锈钢会导致回球不顺畅。
	回球槽最低点应与出球机活动托板持平。	是口 否口		如回球槽最低点不高于进球口会导致无法正常回球。
活动板	按图纸尺寸留好活动板，出线口按图纸尺寸开好。	是口 否口		如未开孔会导致控制线无法安装。
投影	投影机吊架按图纸尺寸固定牢固，承重25KG。	是口 否口		如现场情况没有做加固处理，会造成投影仪挂不上。
常电电源	投影插座1个，传感器插座2个，地面插座1个，天地需预留电源线。	是口 否口		如未留插座会导致设备无法正常使用。
开关	开关已装好，能有效控制镜面一体机，传感器，投影机及TEE射灯。	是口 否口		如无开关控制会减少设备的使用寿命。
灯孔	Tee射灯灯孔已开120mm,明装不需开孔，电源线穿出天花。	是口 否口		如不开孔会导致灯具无法安装。
天花加固	传感器位置是否加固，要求承重5KG。	是口 否口		如现场情况没有做加固处理，会造成传感器无法安装。
线材检查	感测器千兆网线、HDMI高清是否预埋到位。	是口 否口		如现场情况没有按要求预埋会影响感测器安装，投影机的安装。
整改建议：			复核人签名：	
装修复核需要带一把7米卷尺：			复核日期：	

CLIENT.建设单位

PROJECT TITLE.项目名称

DRAWING TITLE.图名

项目装修复核检查表

REVISIONS.版本

第一版

第二版

第三版

制图.

SCALE.
比例 1:30

DATE.
日期 2025.8

版权所有

施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
d e
中 城chak n命油
d in

,工地状况，建筑结构设计图及有关图

出图专用章 图纸无效

图幅：A4
SHEET NO.图号

DL-01

Project Renovation Review Checklist

Project name	American Golf Cages Golf Party			
Project address	America			
Scope of examination	Content details	Is it qualified?	Full scale	Remarks
Mub	The 12mm thick flame-retardant version of the corner iron around the curtain should extend at least 80mm.	Yes No		If the gap between the curtain and the ground is less than 80mm, the curtain will have large gaps around it after installation, which affects its appearance and may cause the ball to fall behind the curtain during play.
	The curtain is 300mm away from the back wall.	Yes No		If the site lacks 300mm, it will hinder the engineer's efficiency in installing the curtain and compromise its flatness.
	The side soft cover surface is 100mm from the side wall, and the soft cover ceiling surface is 100mm from the ceiling.	Yes No		If the available space is less than 150mm, it will hinder the engineer's efficiency in installing the curtain and compromise its flatness.
	The top wooden panel of the curtain should be reinforced to support a load of 50KG.	Yes No		If the site conditions are not reinforced, the curtain may fail to hang properly, causing the entire structure to collapse.
Attack table	The striking table design is complete. (Striking pad dimensions: 1500mm*1800mm/1200mm*1800mm)	Yes No		The area size must be accurate. Any error will affect the entire striking pad area.
	The elevation of the striking pad's sunken area shall be 25mm lower than the striking platform, and must comply with the dimensional specifications in the drawings.	Yes No		The area size must be precise. Any error will cause the entire striking pad to become raised or depressed.
Buffer slope	The buffer slope design is complete, and its lowest point must be higher than the embedded part's inlet.	Yes No		If the lowest point of the return hole is not higher than the goal hole, the ball will not be returned normally.
	The dimensions meet the drawing requirements.	Yes No		If the specifications are not met, the camera will not function properly.
Return groove	The stainless steel must be properly attached as specified, ensuring it does not exceed the wooden board surface.	Yes No		If the stainless steel is not attached, the ball will not return smoothly.
	The lowest point of the return groove should be level with the movable tray of the ball machine.	Yes No		If the lowest point of the return groove is not higher than the goal, the ball will not be returned normally.
Mobile boards	Prepare the movable panel according to the drawing dimensions, and drill the wire outlet in the same size.	Yes No		If the hole is not opened, the control line cannot be installed.
Projection	The projector bracket is securely mounted to the blueprint dimensions, with a load capacity of 25KG.	Yes No		If the site is not properly reinforced, the projector may fail to mount.
Constant current power supply	One projection socket, two sensor sockets, and one ground socket are required, with power cables reserved for both ground and overhead systems.	Yes No		If the socket is not left, the device will not work properly.
Switch	The switch is now installed, enabling effective control of the mirror-integrated unit, sensors, projector, and TEE spotlight.	Yes No		If there is no switch control, the service life of the equipment will be reduced.
Lamphole	The Tee-shaped spotlight has a 120mm hole opening. For surface-mounted installation, no additional holes are required, and the power cord extends through the ceiling.	Yes No		If the hole is not opened, the lamp cannot be installed.
Roof reinforcement	The sensor must be reinforced at the designated location and capable of supporting a load of 5 kilograms.	Yes No		If the site conditions are not reinforced, the sensor cannot be installed.
Wire inspection	Check if the sensor's Gigabit Ethernet cable and HDMI high-definition port are properly installed.	Yes No		Failure to embed components as required may hinder sensor and projector installation.
RECOMMENDATIONS FOR REFORMS			Reviewer signature:	
a 7 @-@ meter tape is required for the repair review:			Review Date:	

CLIENT. The construction unit

Project Title

Drawing Title.

Project Renovation Review Checklist

REVISIONS.Versions

The front page

The second edition

The third edition

Charting .

SCALE. 1:30

Proportion

DATE.

Date 2025. 8

All right reserved

The construction unit must verify the dimensions on-site. If any discrepancies are found, the design unit must be notified immediately.

d e

Chak N Life Oil

d in

Construction site conditions, architectural structural design drawings and related diagrams

Drawing-specific seal,drawings invalid

Image size: A4

Sheet No.

DL-01

装修设计总说明(一)DESIGN DEVELOPMENT CONSTRUCTION DRAWING DESCRIPTION

一、设计及施工依据：

1.甲方提供的建筑施工图纸、确认的平面布置及相关的方案、效果图等资料。

2.由国家建设部颁发的<<建筑装修工程施工及验收规范>>(GB.50210-2001)。

3.由国家建设部，技术监督局联合发布的<<建筑内部装修设计防火规范>(GB50222-2017)。

4.<<建设电气安装工程质量检验评定标准>>(GB50303-2015)。

5.装饰工程施工的标准做法及惯常方式，施工图中未详尽之做法请参照相关标准及工具书；如：中国建筑工业出版社<装饰工程施工手册>>等。

二、设计规模及范围：

1.本装饰工程为：————美国高尔夫球舱高尔夫派模拟器项目设备安装工程。

2.本装饰工程范围为：缓冲区、打击区、休闲区。

3.工程地址：-------美国

三、设计标高和定位及其它：

1.本装饰工程设计相对标高±0.000为建筑装饰完成标高，相对与原建筑标高，根据不同地面装饰材料相应地提高，定位详见各部分施工图。

2.本设计尺寸均为完成面尺寸，现场如有较小出入，可适当调整。

3.本设计所注尺寸以毫米为单位，标高以米计。

4.此高尔夫设备安装施工图只包含GolfⅠⅡ模拟器安装部分，消防、通风、空调需由专业公司提供图纸。

5.本图所示墙、柱等相对尺寸为控制尺寸，标高、位置、尺寸必须现场放线而定，且须由设计人员认定后方可施工。

6.所有图纸尺寸核查与现场有误差时，施工者必须与技术人员或设计师联系，做尺寸修正，以补充或变更设计图纸为最新高尔夫设备安装施工图。

7.地台标高均为木工完成面标高，天花标高为从地面到天花的相对标高。

8.天花部分须完成本套高尔夫设备安装施工图要求的施工部分。投影仪以投影仪安装公司要求为准，图纸所标投影仪相关尺寸仅作参考。

9.所有隐蔽工程木工部分均按国家有关规定刷防火，防腐漆。防火涂料应到消防部门指定的销售点购买，并附有质量检测报告后方可封闭

10.本工程选用材料必须符合国家有关建筑装修材料有害物质限量标准的规定。。

11.本高尔夫设备安装施工图中与空调、电器、给排水、消防有冲突之处，需协调各专业工程现场解决。

12.施工中设计师有权对所有图纸做局部调整(与业主及工程师协商同意的基础上)。。

13.本工程高尔夫设备安装施工图尺寸以毫米(mm)为单位，标高以米(m)为单位。。

14.本工程地台龙骨及面板均采用15厘大芯板、软包基础采用12mm厚阻燃版。软包采用阻燃防火2层3cm过滤棉填充层、夹层使用3mm阻燃防火胶垫+面层使用麻布布艺。所用材料必须符合环保要求，严禁使用国家明令淘汰的材料。

15.各工序必须严格按国家《建筑装饰装修工程验收规范》执行。

一、模拟高尔夫设备配电要求：

1.超清4k激光投影仪功率---380W

2.镜面一体机功率—650W

3.全自动智能上球机功率—-110W。

4.高速视觉传感器—(150W电流0.9A;电压220V)。

注：除以上数据外其它的设备功率都小于280T,整体设备220V的电压都能满足。所有电源、插座、开关、气管、数据线、信号线等线路全部套线管，布暗线，强电弱电必须分开套管。

CLIENT.建设单位

PROJECT TITLE.项目名称

DRAWING TITLE.图名

装修设计总说明

REVISIONS.版本

第一版

第二版

第三版

制图.

SCALE.
比例 1:30

DATE.
日期 2025.8

版权所

施工单位须现场校验尺寸
如有不符须立即通知设计单位

备注：Notes

应与说明，工地状况，建筑结构设计图及有关图
是度图解 应以图中所注尺寸为准，最终

图幅：A4
SHET NO.图号

DL-05

General Description of Interior Design (Part 1) DESIGN DEVELOPMENT CONSTRUCTION DRAWING DESCRIPTION

1. Design and Construction Basis:

1. The construction drawings, confirmed floor plans, and related design proposals and renderings provided by Party A.
2. The "Code for Construction and Acceptance of Building Decoration Works" (GB.50210-2001) issued by the Ministry of Construction.
3. The 'Fire Protection Code for Interior Decoration Design of Buildings' (GB50222-2017), jointly issued by China's Ministry of Housing and Urban-Rural Development and the General Administration of Quality Supervision, Inspection and Quarantine.
4. "Code for Quality Inspection and Evaluation of Electrical Installation Works" (GB50303-2015).
5. The standard practices and common methods for decoration engineering construction should be referred to relevant standards and reference books for those not detailed in the construction drawings, such as: China Building Industry Press <Decoration Engineering Construction Manual> and so on.

II. Design Scope and Scale:

1. This decorative project involves the installation of equipment for the American Golf Cabin Golf Simulator.
2. The scope of this decoration project includes: buffer zone, impact zone, and leisure zone.
3. Project Address: -------United States

3. Design elevation, positioning, and other details:

1. The finished elevation of this decoration project is set at ±0.000 relative to the building's original elevation, with adjustments made according to the specific flooring materials used. Detailed positioning specifications are provided in the respective construction drawings.
2. All dimensions in this design are for finished surfaces. Minor deviations may be adjusted on-site as needed.
3. All dimensions in this design are in millimeters, and elevations are in meters.
4. This golf equipment installation plan covers only the GolfII simulator setup, while fire safety, ventilation, and air conditioning systems require drawings from specialized contractors.
5. The relative dimensions of walls and columns shown in this drawing are control dimensions. Elevation, position, and dimensions must be determined through on-site layout and approved by the designer before construction.
6. If any discrepancy is found between the verified dimensions on drawings and the actual site conditions, the construction team must contact technical personnel or designers to make necessary adjustments. This involves updating or modifying the design drawings to ensure they reflect the latest specifications for golf equipment installation.
7. The floor elevation is the finished surface elevation of the carpenter, and the ceiling elevation is the relative elevation from the floor to the ceiling.
8. The Tianta section shall complete the construction work specified in the installation drawings for this golf equipment set. The projector shall comply with the requirements of the projector installation company, and the dimensions of the projector marked on the drawings are for reference only.
9. All concealed works and carpentry parts shall be coated with fireproof and anti-corrosion paint in accordance with relevant national regulations. The fireproof coating must be purchased from designated sales points authorized by the fire department and accompanied by a quality inspection report before sealing.
10. The materials used in this project must comply with the national standards for the limits of harmful substances in building decoration materials.
11. Any conflicts between this golf equipment installation plan and HVAC, electrical, plumbing, or fire protection systems must be resolved through on-site coordination among all relevant disciplines.
12. During construction, the designer may make minor adjustments to all drawings, provided such changes are approved by the owner and the engineer.
13. The dimensions in this project's golf equipment installation drawings are in millimeters (mm), and elevations are in meters (m).
14. The project's floor joists and panels are constructed with 15mm thick core panels, while the soft-sandwich foundation utilizes 12mm thick flame-retardant boards. The soft-sandwich layer contains a 3cm double-layer fireproof cotton filling, with a 3mm flame-retardant rubber pad as the interlayer and a linen fabric surface layer. All materials must comply with environmental standards, and the use of materials explicitly banned by national regulations is strictly prohibited.
15. All the processes must be carried out strictly according to the national "Code for Acceptance of Building Decoration and Renovation Engineering".

1. Power Supply Requirements for Simulated Golf Equipment:

1. Ultra HD 4K laser projector power: 380W
2. Mirror integrated machine power—650W
3. The fully automatic intelligent ball-feeding camera has a power of-110W.
4. High-speed vision sensor (150W current, 0.9A; voltage 220V).

Note: All equipment except those specified above has a power rating below 280T, and the system operates reliably at 220V. All power supplies, sockets, switches, gas pipes, data cables, and signal lines are installed in conduit with concealed wiring, ensuring separate conduits for high-voltage and low-voltage circuits.

CLIENT. The construction unit

Project Title

Drawing Title.

General DESCRIPTION OF THE RECONSTRUCTION DESIGN

REVISIONS.Versions

The front page

The second edition

The third edition

Mapping.

SCALE.

Propo-rtion 1:30

DATE.

Date 2025.8

Copyright

The construction unit shall conduct on-site verification of dimensions.
If any discrepancies are found, the design unit shall be notified immediately.

Notes

It should be noted that the site conditions, building structure design drawings and related drawings should be based on the dimensions indicated in the drawings,ultimately.

Image size: A4

She T No.

DL-05

设备说明 Material description



4k高清激光投影仪

T位射灯

高速视觉传感器



耐冲击幕右布

镜面一体机

落地球杆架

长草+沙坑

全自动智能上球机.

一体按键

高密度带纹路NBR.....

底+3D减震层+灌胶

层+尼龙草）

草皮材质PP+Pe

参考效果图01

CLIENT.建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

REVISIONS. 版本

第一版.

第二版

第三版.

制图.

SCALE.

比例 1:30

DATE.

日 期 2025.8

版权所有
施工时须以标注尺寸为准
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D 市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，军导为，最共尺寸宿在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A4

SHEET NO. 图号

Device Description Material description



.....4K HD laser projector

T-position spotlight ·.....

..... high-speed vision sensor



Impact-resistant curtain right panel.....

.....Mirror-in-One Machine

Earth rod frame

..... Grass + bunker..

Fully automatic intelligent ball-feeding machine.....

.....one button

.....High-density textured NBR.....

... The turf material is made of PP+Pe.

Bottom + 3D shock-absorbing

layer + glue layer+nylon grass)

Reference rendering 01

CLIENT. Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE.Title of the drawing

REVISIONS. 版本

charting .

SCALE.

Proportion 1:30

DATE.

date 2025.8

all right reserved
施工时须以标注尺寸为准
施工单位须现场校验尺寸
If any discrepancies are found, the design unit shall be notified immediately.
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
The most common dimensions of the missile are as follows:
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A4

Sheet No.

空间材质说明 Equipment description



参考效果图02

CLIENT. 建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

REVISIONS. 版本

第一版

第二版

第三版

制图.

SCALE. 比例 1:30

DATE. 日期 2025.8

版权所有
施工时须以标注尺寸为准
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D 市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects


备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，，只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A4

SHEET NO. 图号

Space Material Description Equipment description

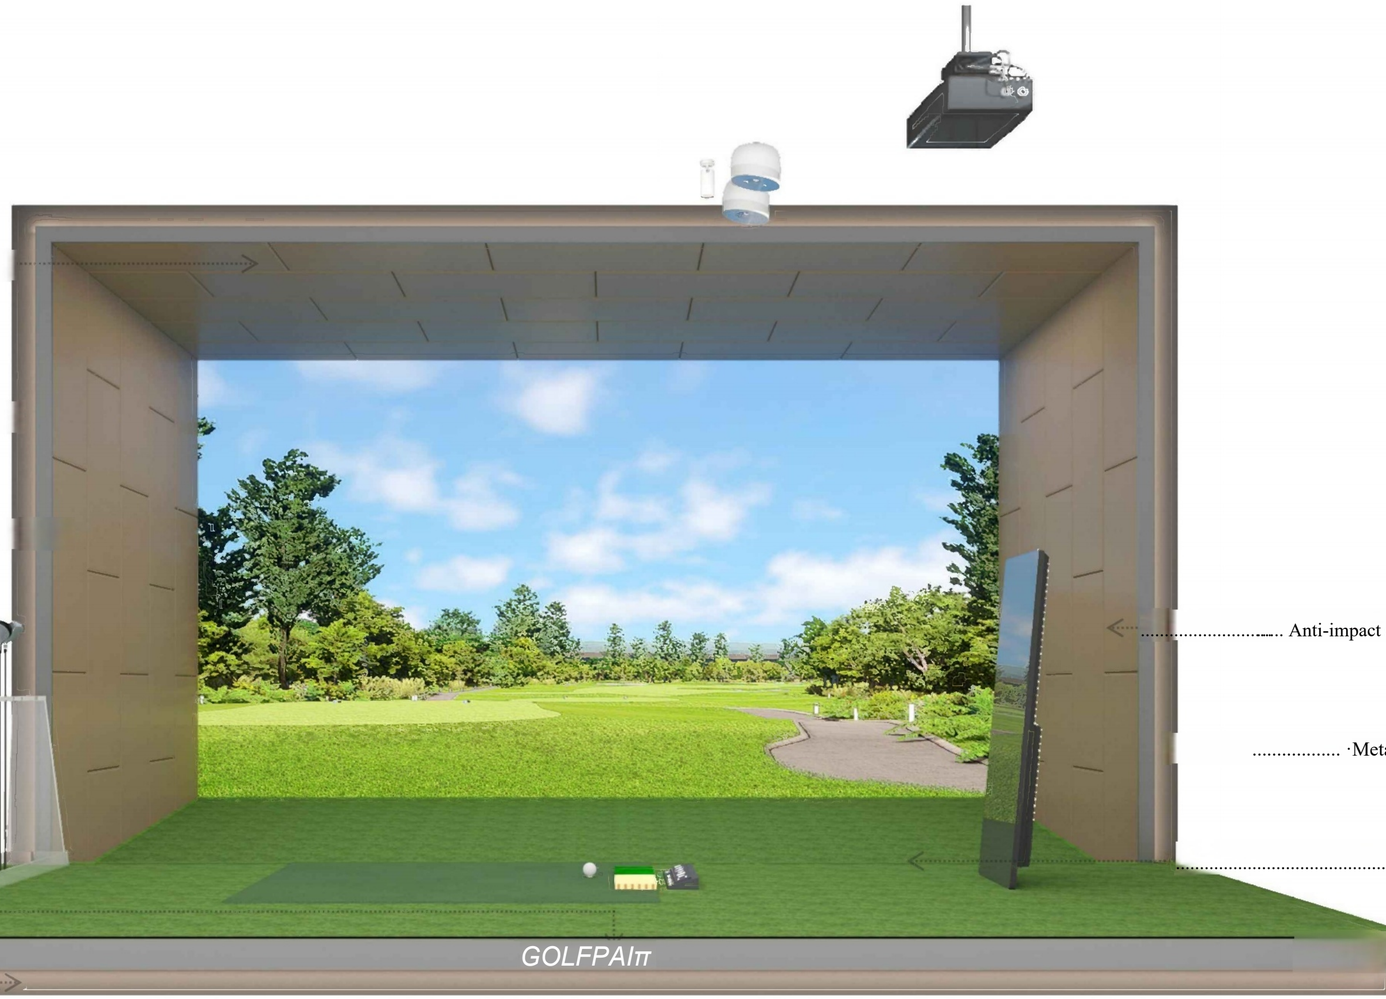

Impact-resistant soft-pack ceiling...

Metal trim strips concealing hidden LED strips.....

Anti-impact soft package wall surface.....

Anti-impact soft package wall surface

·Metal trim strip concealing a light strip

Return Slot (Metal Trim)

Acrylic light-up logo

金属条

...The edge strip contains hidden light strips

Reference rendering 02

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE.Title of the drawing

REVISIONS. Versions

First edi-
tion Sec-
ond edit-
ion Third
edition

charting .

SCALE.
scale 1:30

DATE.
date. 2025.8


all right reserved
施工时须以标注尺寸为准
施工单位须现场校验尺寸
If any discrepancies are found, the design unit shall be notified immediately.
This drawing is copyright
D City h woknedan1bo
Contractor must check all dimensions on site
Contractor must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
Use,, only with, the maximum size is based on
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A4

Sheet No.

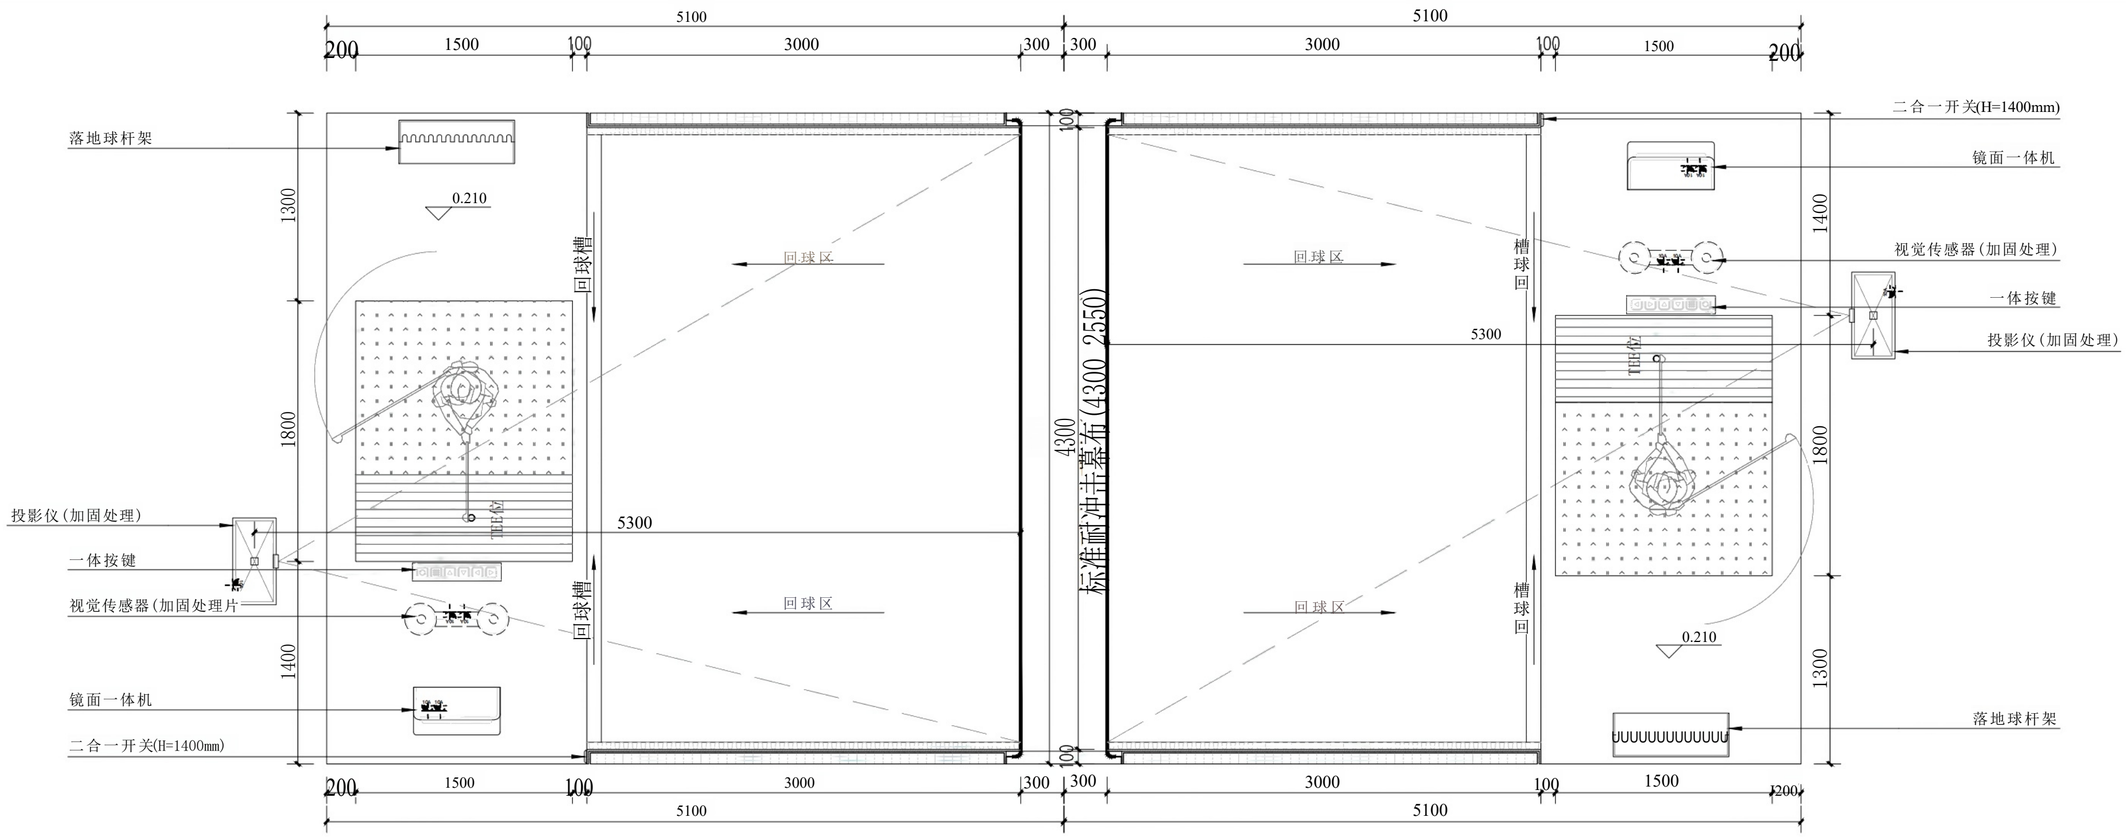

平面图130

注：设计范围为高尔夫派模拟器设备安装区域
高尔夫区域总高度H=3.0m
图纸所有标高以毛坯地面找平为±0.00mm
如需增加影音。K歌等功能，音响设备需专业技术人员深化图纸。

CLIENT.建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

高尔夫派S1

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2


版权所有
施工时须以标注尺寸为准
施工单位须现场核查尺寸
如有不符须立即通知设计单位
This drawing is copyright
D 市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，， 只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

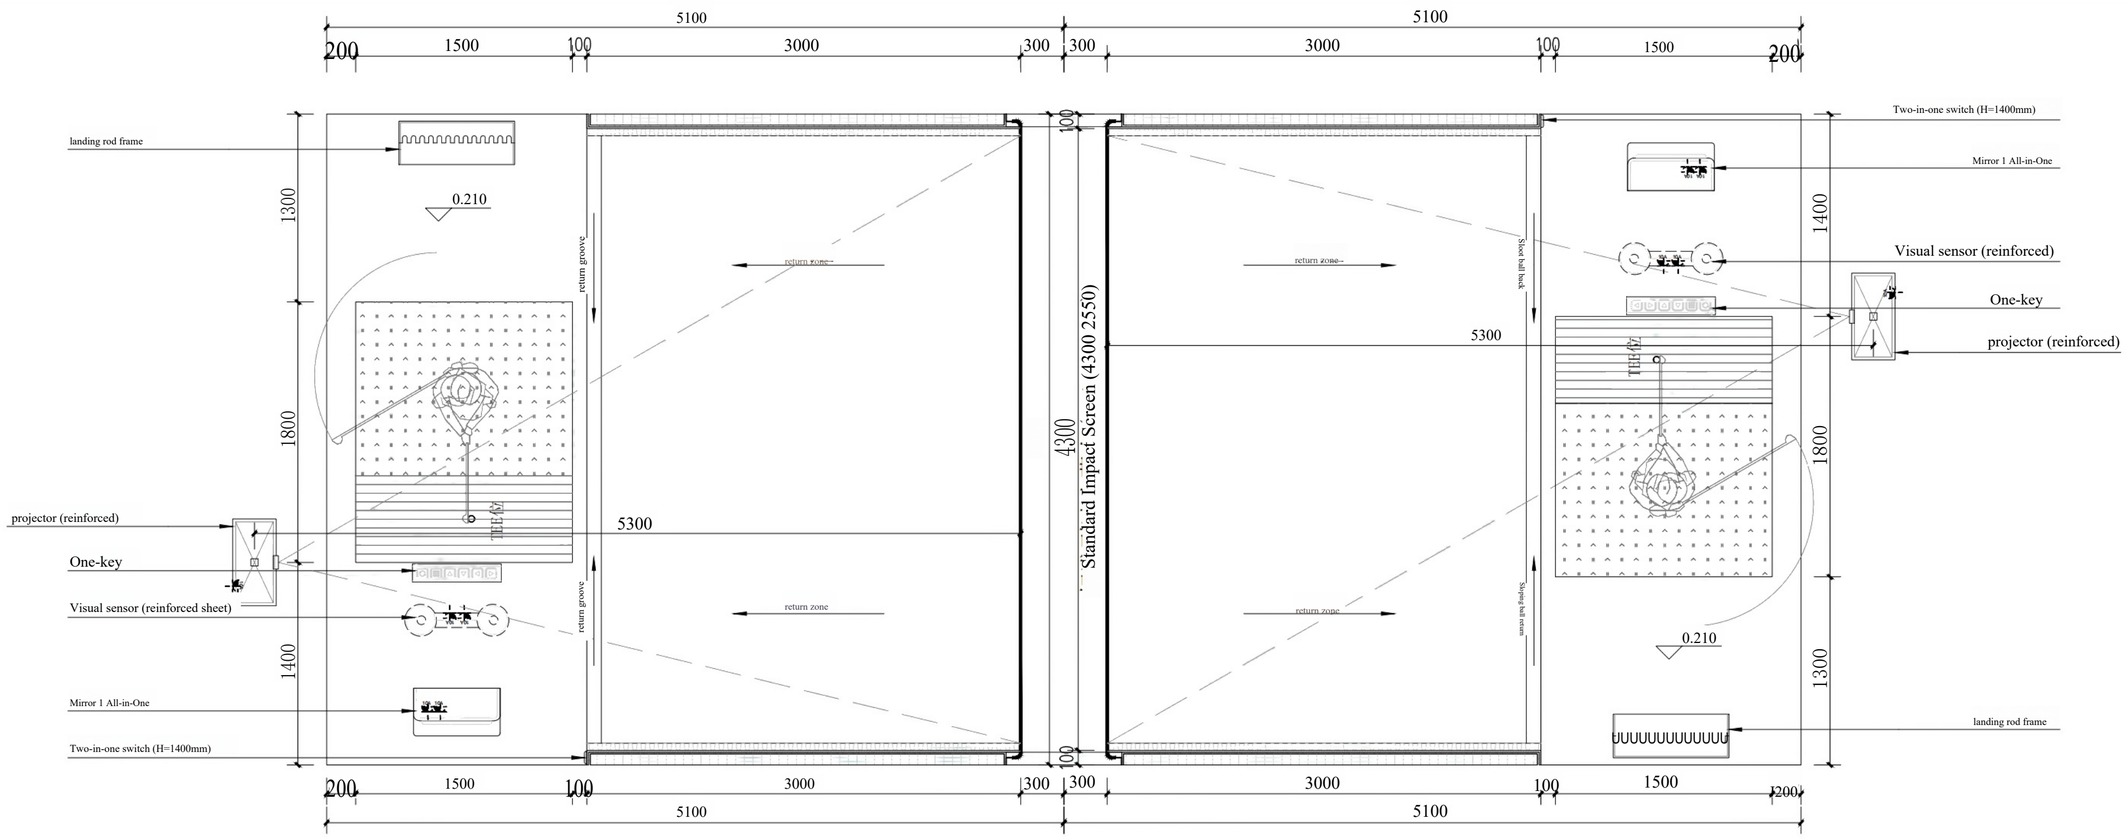

Plan 130

Note: The design scope covers the total height H=3.0m of the golf area where the golf simulator device is installed.

All elevation measurements in the drawings shall be ±0.00mm based on the rough ground leveling.

To add features like audiovisual and karaoke, the audio equipment requires professional technicians to refine the technical drawings.

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE.Title of the drawing

unit type 。

Golf S1

charting

SCALE.

scale 1:30

DATE.

date 2026.2. 。

all right reserved

All construction measurements shall be based on

[illegible] must

be immediately reported to the design unit.

This drawing is copyright

D City h wokmedan1bo

Contractors must check all dimensions on site

Contractors must be notified immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。

2.本图纸应与说明，工地状况，建筑结构设计图及有关图


need Only for the maximum size according to

4.除特别注明外，图中所有尺寸均为毫米单位。


5.未签出图专用章，图纸无效。

Image size: A2


Sheet No.

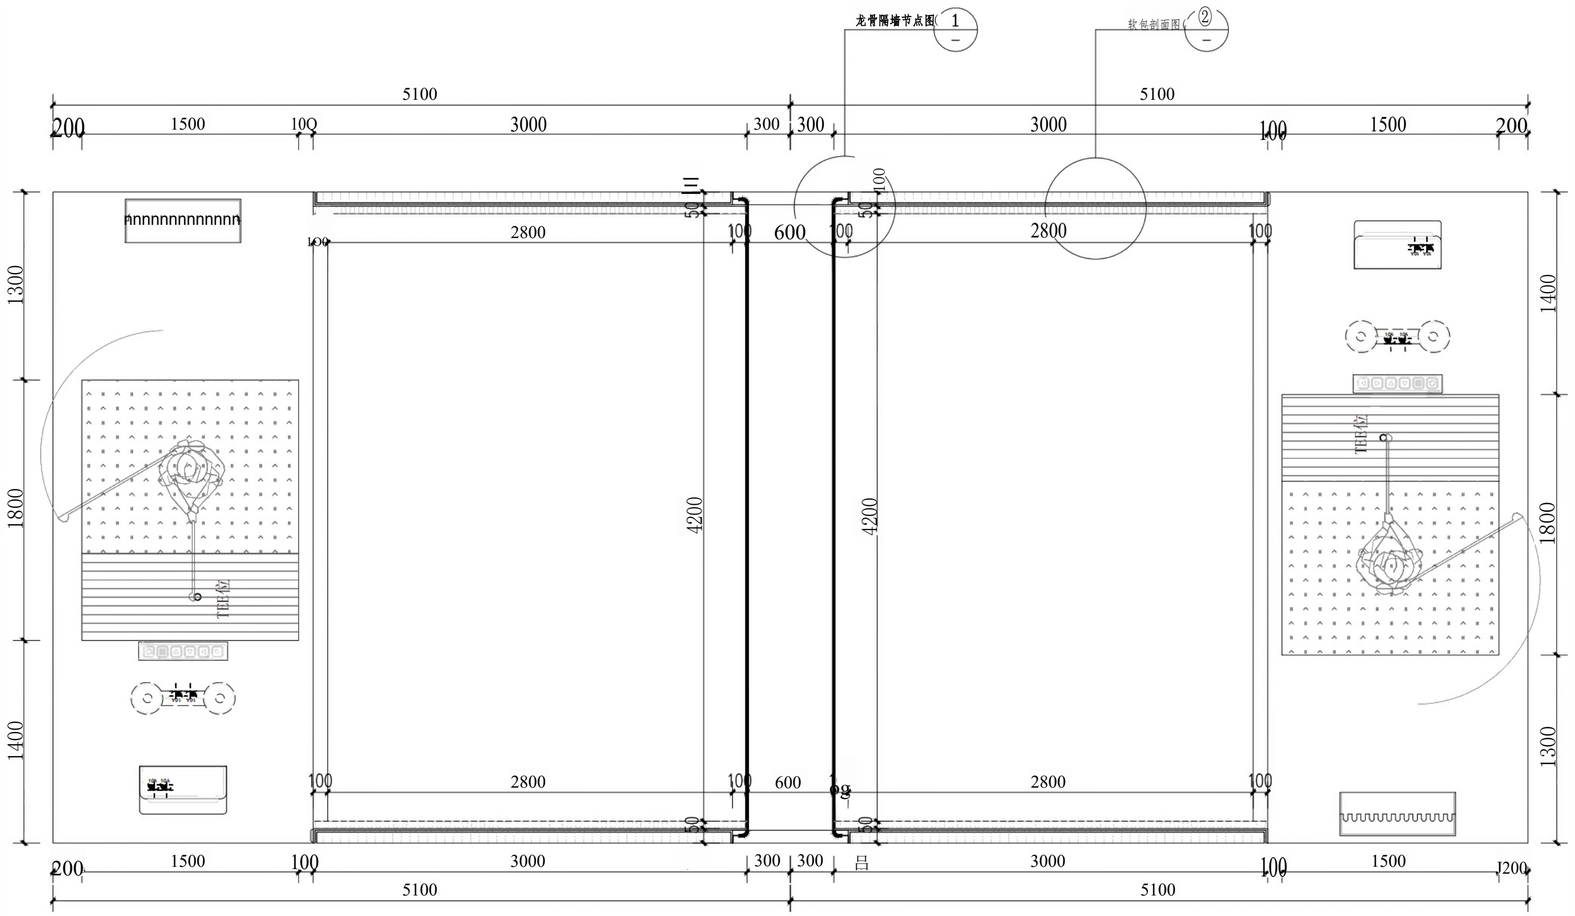


龙骨隔墙尺寸图130



货架角钢示意图

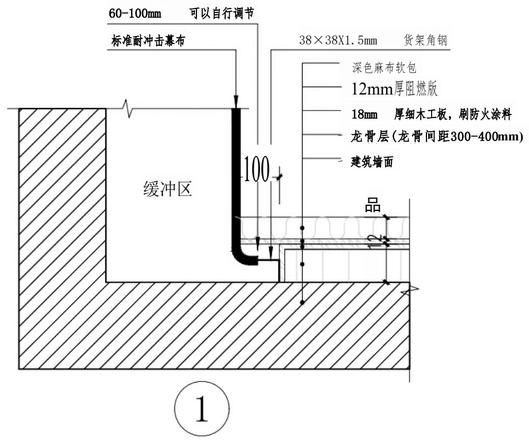

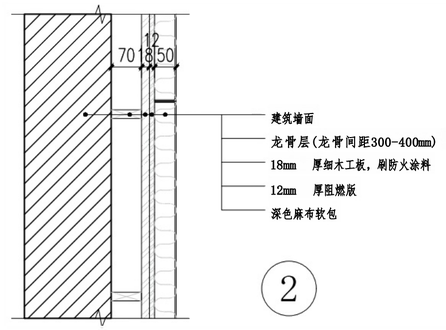

注：请确保缓冲区/打击台/墙面软包龙骨间距需保持300-400mm之内，
幕布四周(左右墙面/天花及缓冲区地台)固定角钢的位置需探出龙骨60-100mm之内，方便走角钢挂件。

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2


版权所有
施工时须以标注尺寸为准
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes


1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，，只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2


SHEET NO. 图号

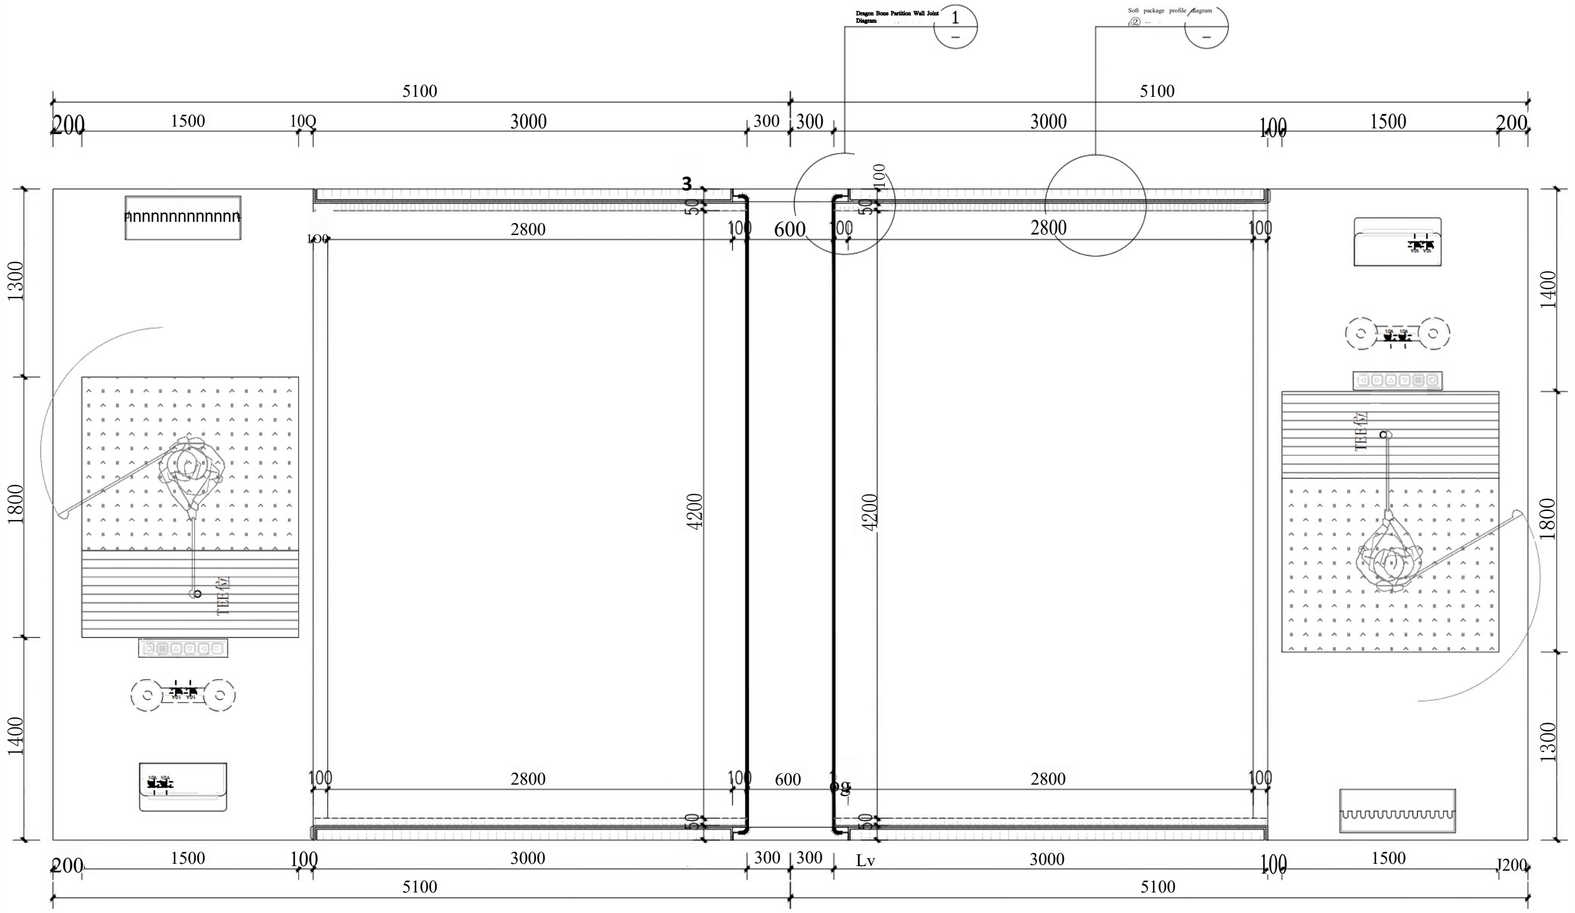


Dimensional drawing of dragon bone partition wall 130



Schematic Diagram of Shelf Angle Steel

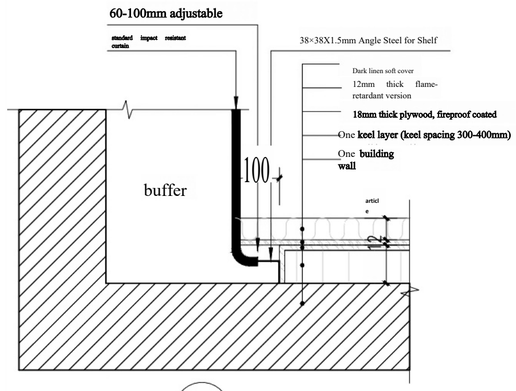

1

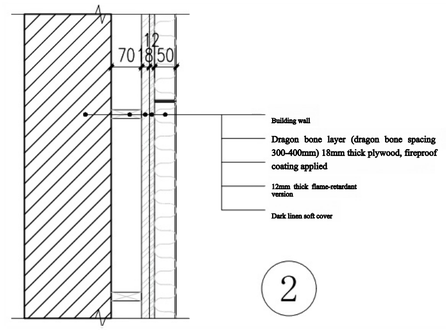

2

Note: Maintain a 300-400mm spacing between the buffer zone, impact pad, and wall soft packaging keel. The angle steel fixing points around the curtain (left/ right walls, ceiling, and buffer zone floor) should extend 60-100mm beyond the keel to facilitate the installation of angle steel hangers.

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图 名

unit type .

Mapping.

SCALE.

Propo-rtion 1:30

DATE.

Date . 2026.2


all right reserved
The marked dimensions shall be taken as the standard during construction.
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes


1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
need
Only for the maximum size according to
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A2


Sheet No.

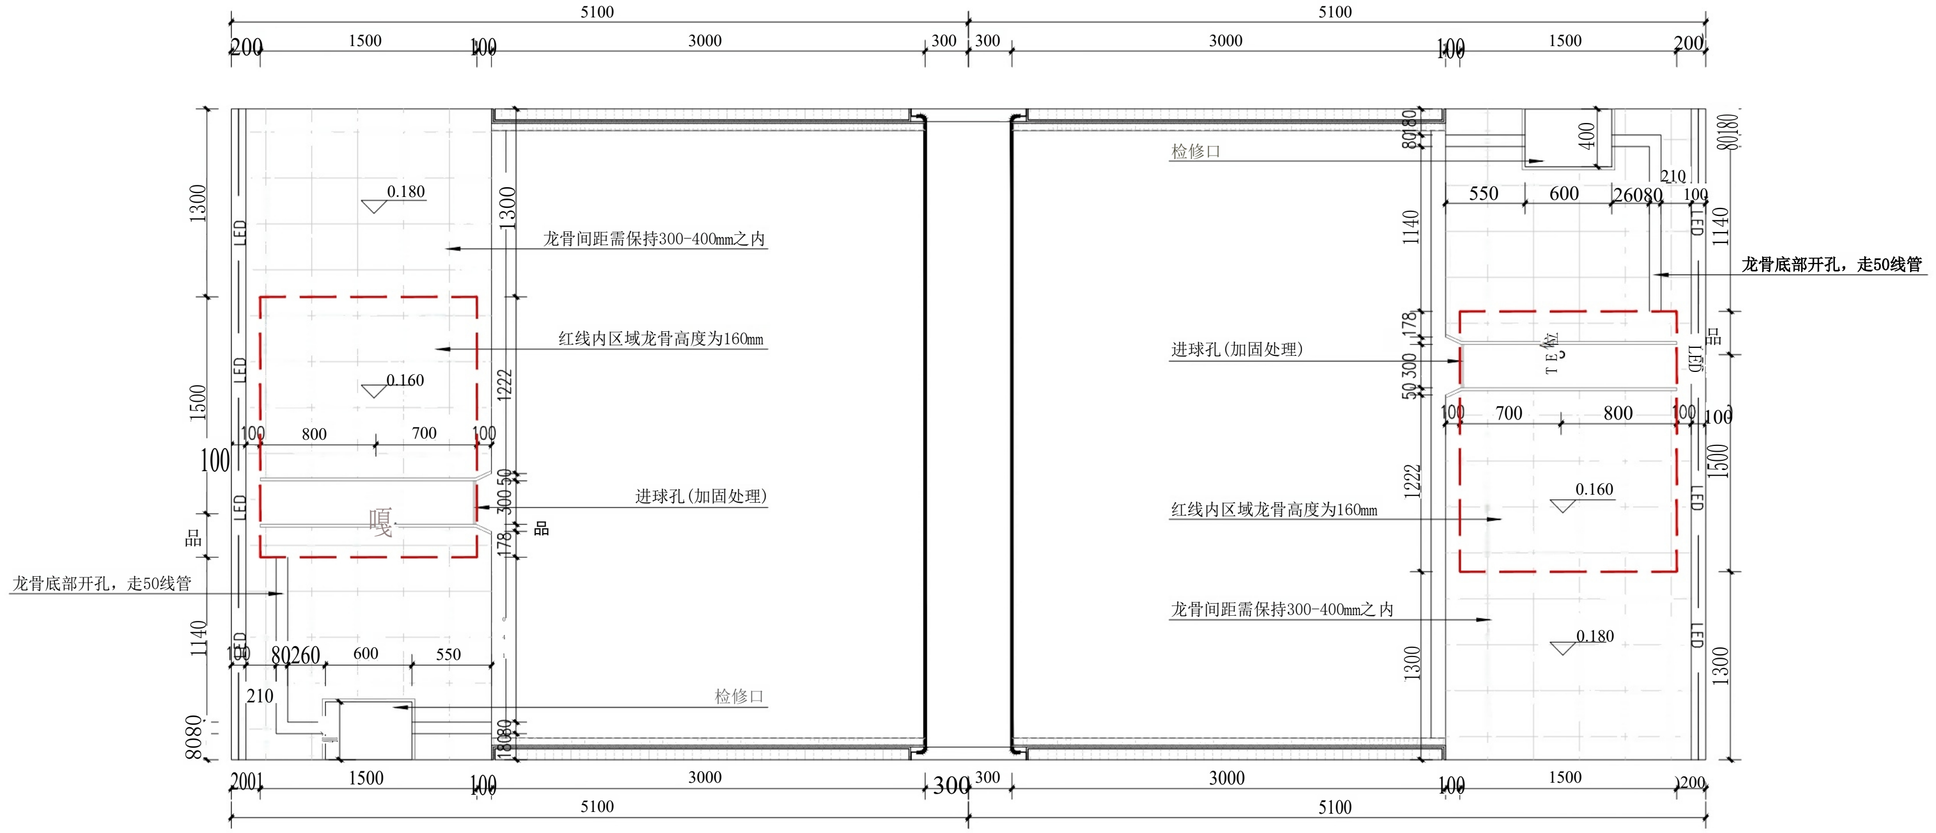


打击台龙骨定位图1:30



龙骨底部开孔剖面图 1:10



进球孔剖面图 1:10



上球机侧面图 1:10

注：请确保缓冲区/打击台/墙面软包龙骨间距需保持300-400mm之内，
幕布四周(左右墙面/天花及缓冲区地台)固定角钢的位置需探出龙骨60-100mm之内，方便走角钢挂件。

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图 名

设备型号.

制图.

SCALE.
比例 1:30


DATE.
日 期 2026.2

版权所有
施工时须以标注尺寸为准
施工单位须核对检查尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects


备注:Notes
1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明、工地状况、建筑结构设计图及有关图
用 。 只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图 幅：A2


SHEET NO. 图号

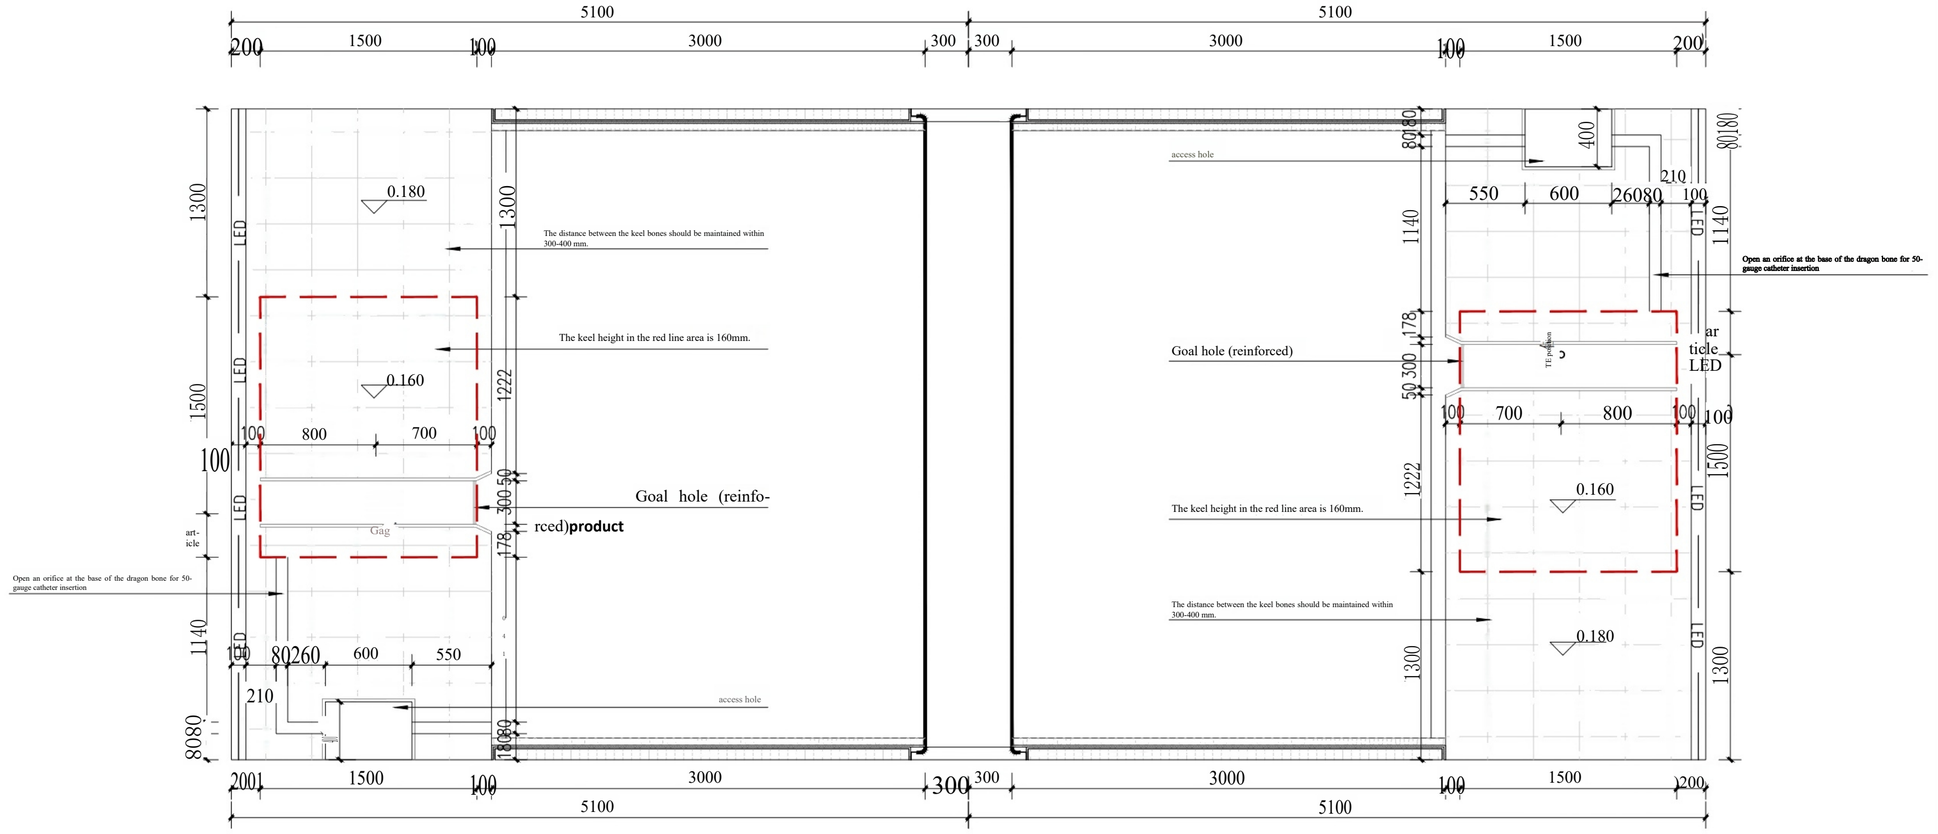


Positioning diagram of the strike plate for the dragon bone
1:30



Cross-sectional view of the bottom opening of the dragon bone
1:10



Goal hole profile 1:10



Side view of the camera 1:10

Note: Ensure the spacing between the buffer zone, impact platform, and wall soft packaging keel is maintained within 300-400mm.

The angle steel brackets should extend 60-100mm beyond the keel at the perimeter of the curtain wall (including left/right walls, ceiling, and buffer zone floor) to facilitate bracket installation.

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图 名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date . 2026.2

all right reserved


The marked dimensions shall be taken as the standard during
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
need
Only for the maximum size according to
3.除特别注明外，图中所有尺寸均为毫米单位。
4.未签出图专用章，图纸无效。

Figure size: A2

Sheet No.

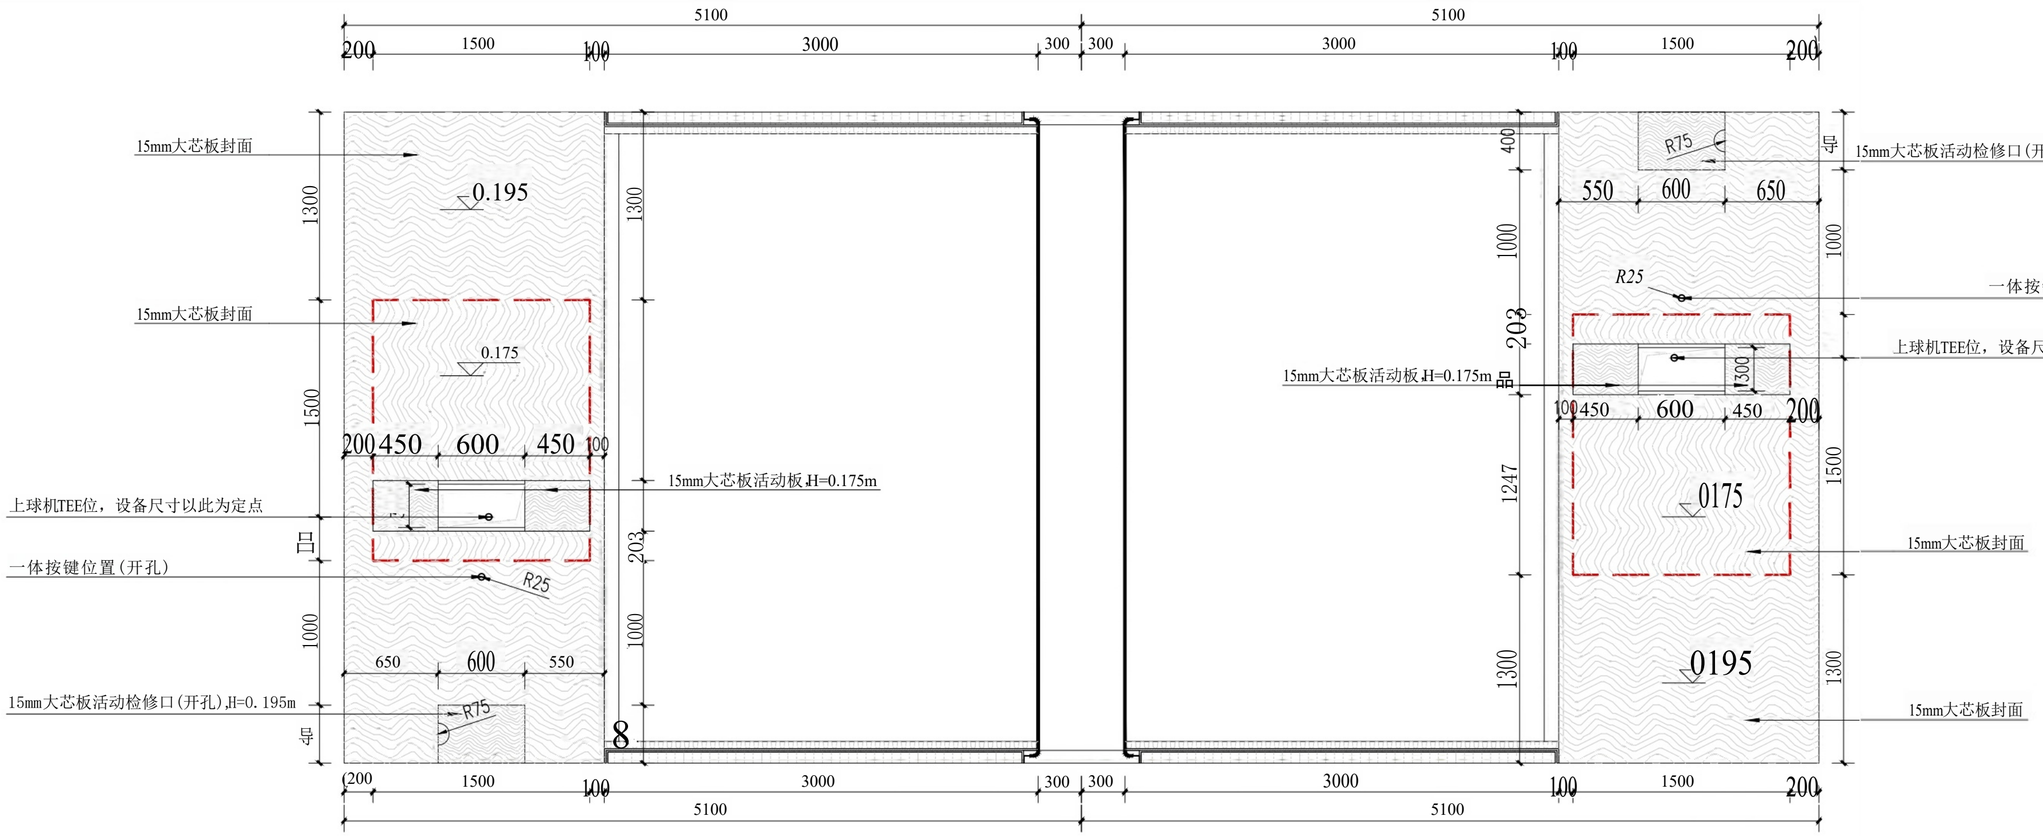

打击台封板图130

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图 名

设备型号.

制图.

SCALE.
比例 1:30

DATE.
日期 2026.2

版权所有
施工时须以标注尺寸为准
施工单位须核对检查尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
[illegible] 用 [illegible] ， 只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

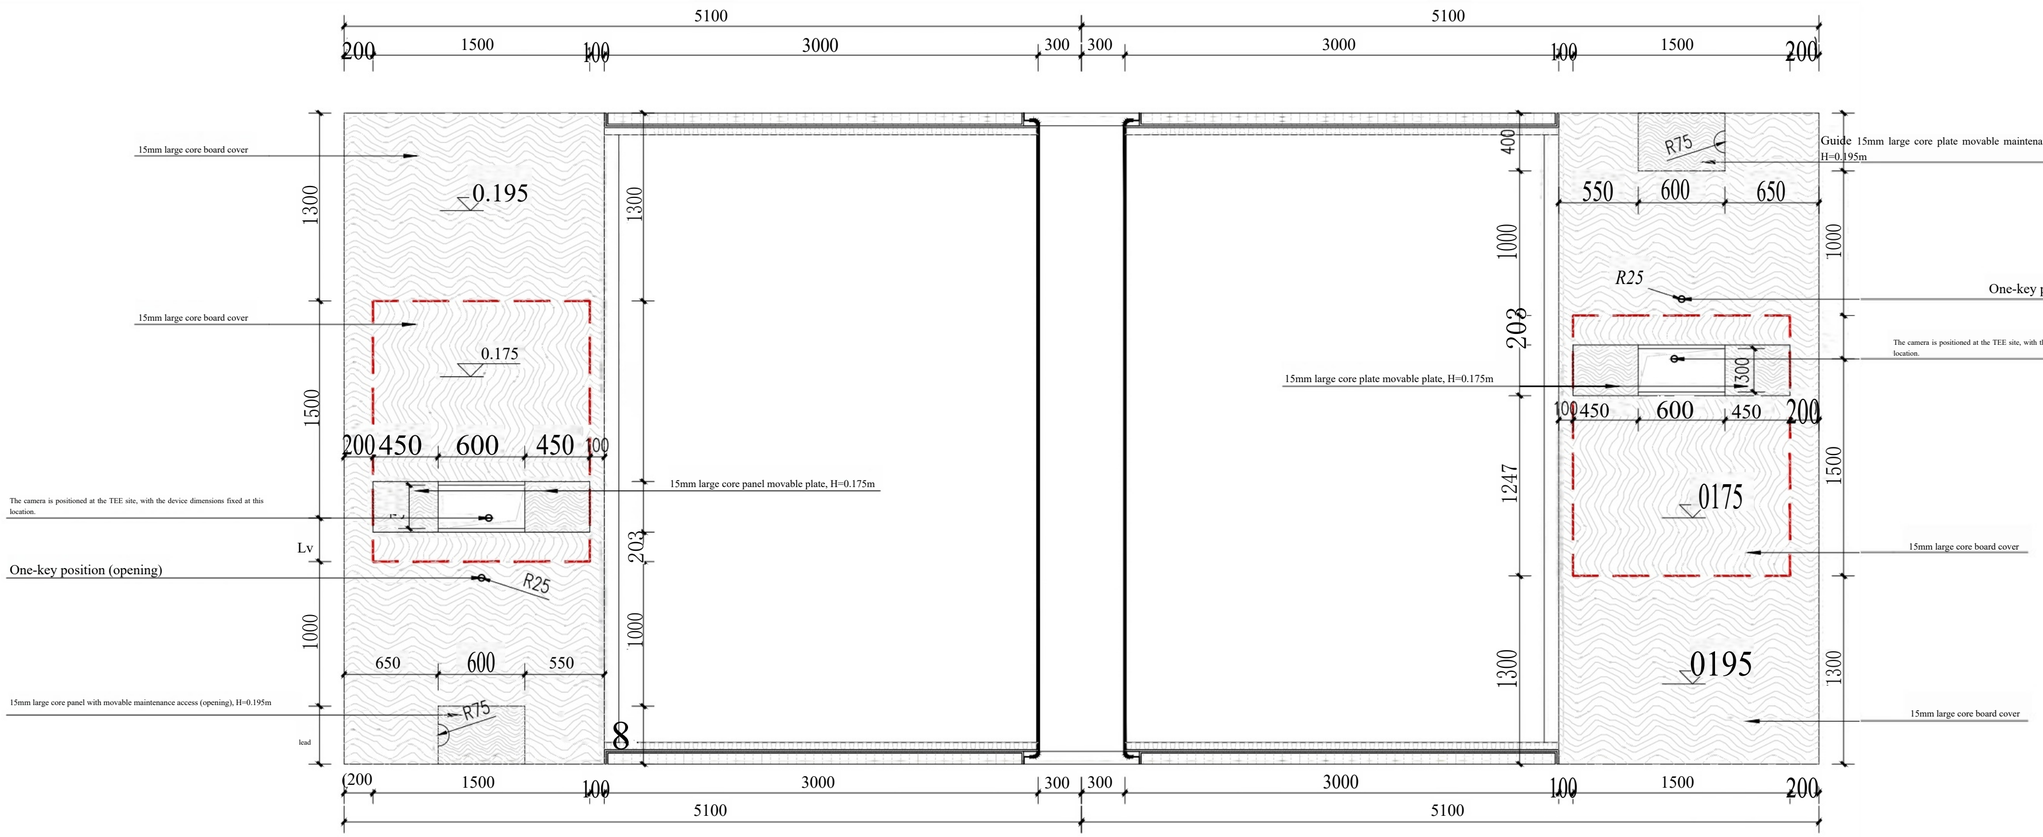


Plate 130 of the Strike Table

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图 名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date . 2026.2

all right reserved


The marked dimensions shall be taken as the standard
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
need
Only for the maximum size according to
3.
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Figure size: A2

Sheet No.

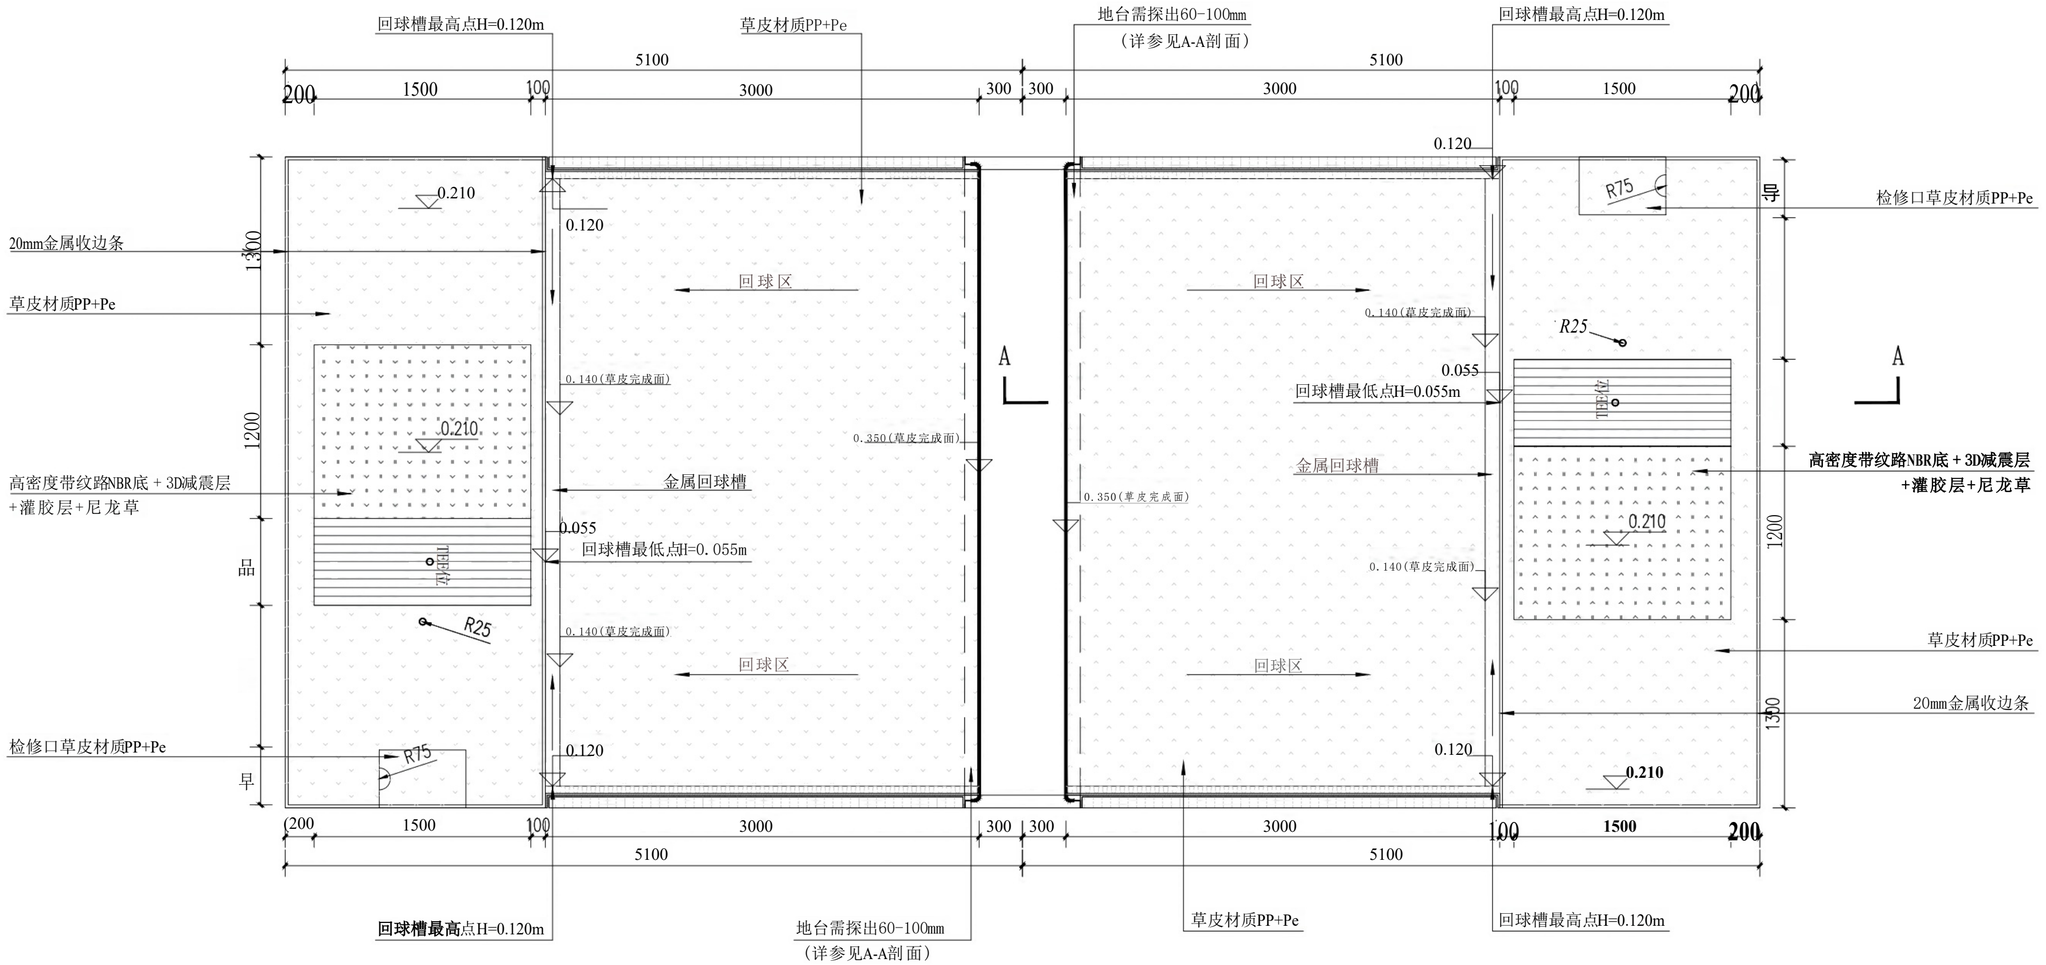

打击台草皮图130

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图 名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日 期 2026.2

版权所有

施工时须以标注尺寸为准

如有不符须立即通知设计单位

This drawing is copyright

Contractor must check all dimensions on site

Contractor must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。

2.本图纸应与说明，工地状况，建筑结构设计图及有关图


用 ，， 只与为，最尺寸据在

4.除特别注明外，图中所有尺寸均为毫米单位。

5.未签出图专用章，图纸无效。

图 幅：A2

SHEET NO. 图号

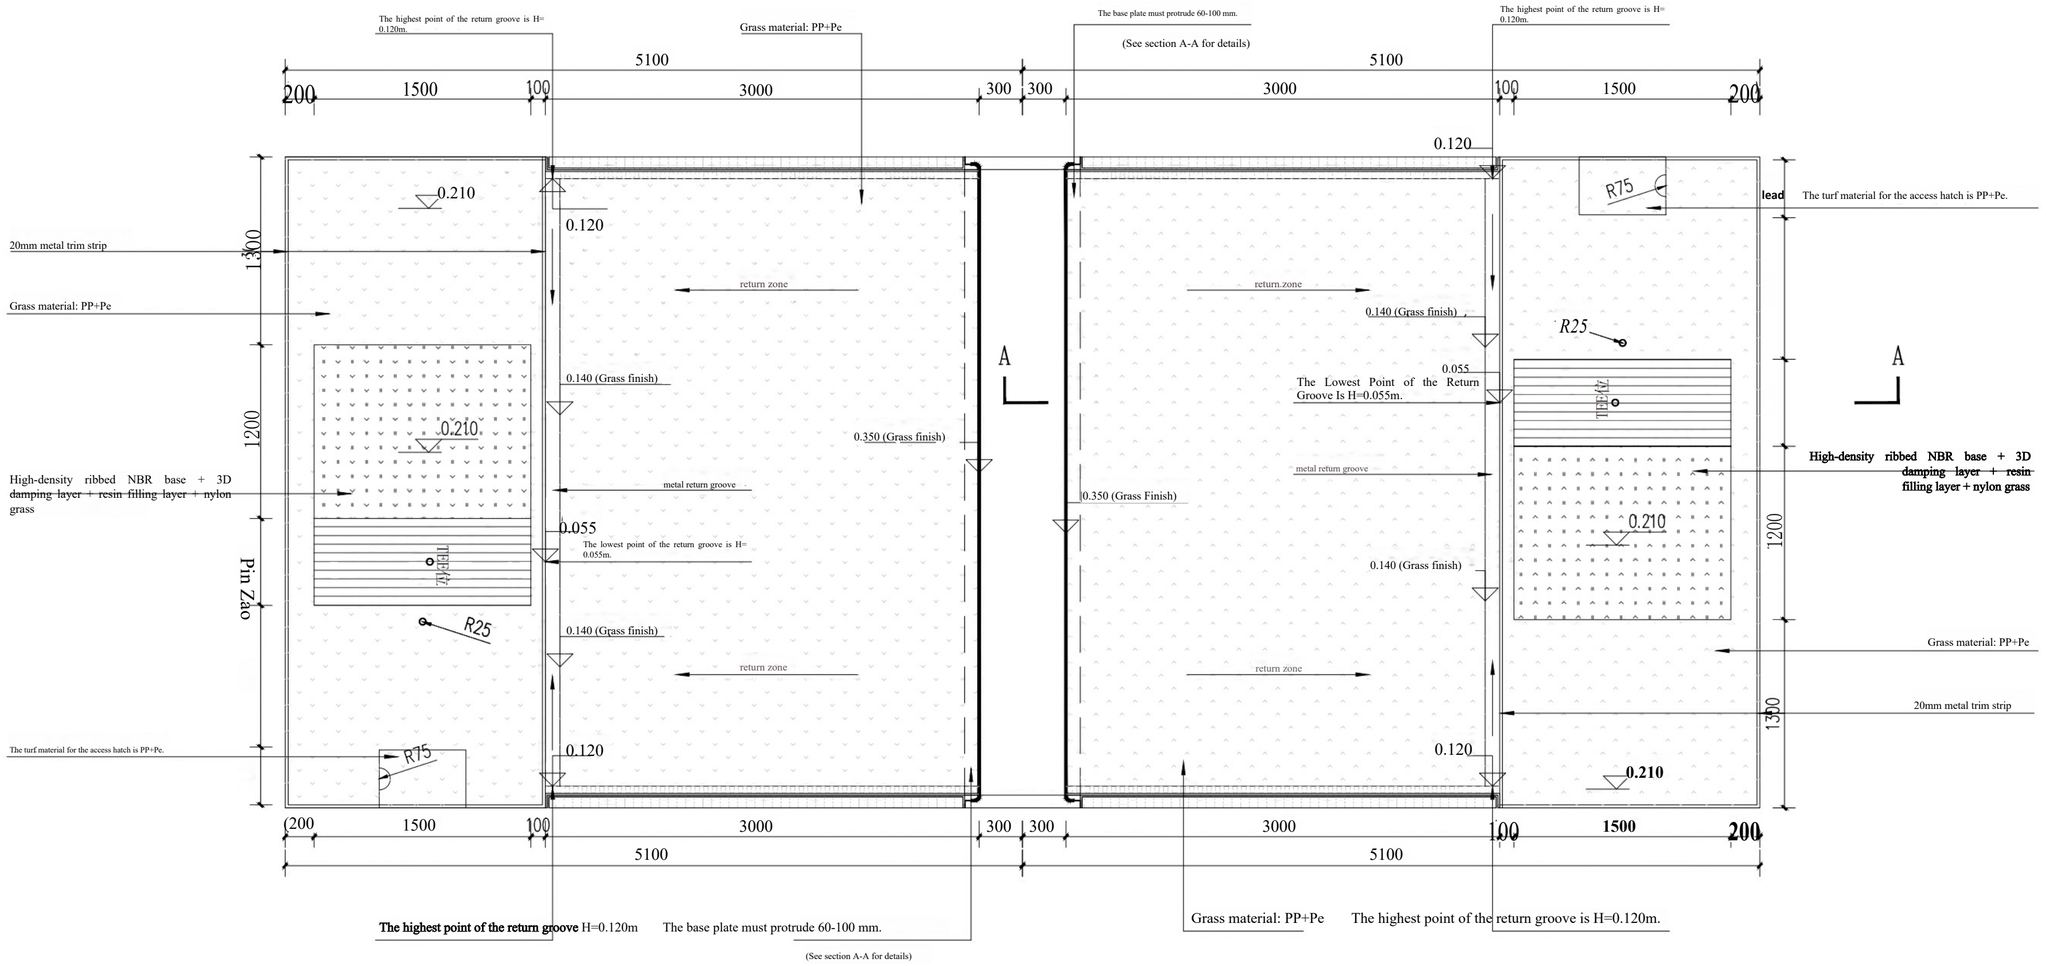

Crush the Turf in Figure 130

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图 名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date . 2026.2

all right reserved


The marked dimensions shall be taken as the standard during
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸同与说明，工地状况，建筑结构设计图及有关图
need
Only for the maximum size according to
3.除特别注明外，图中所有尺寸均为毫米单位。
4.未签出图专用章，图纸无效。

Figure size: A2

Sheet No.

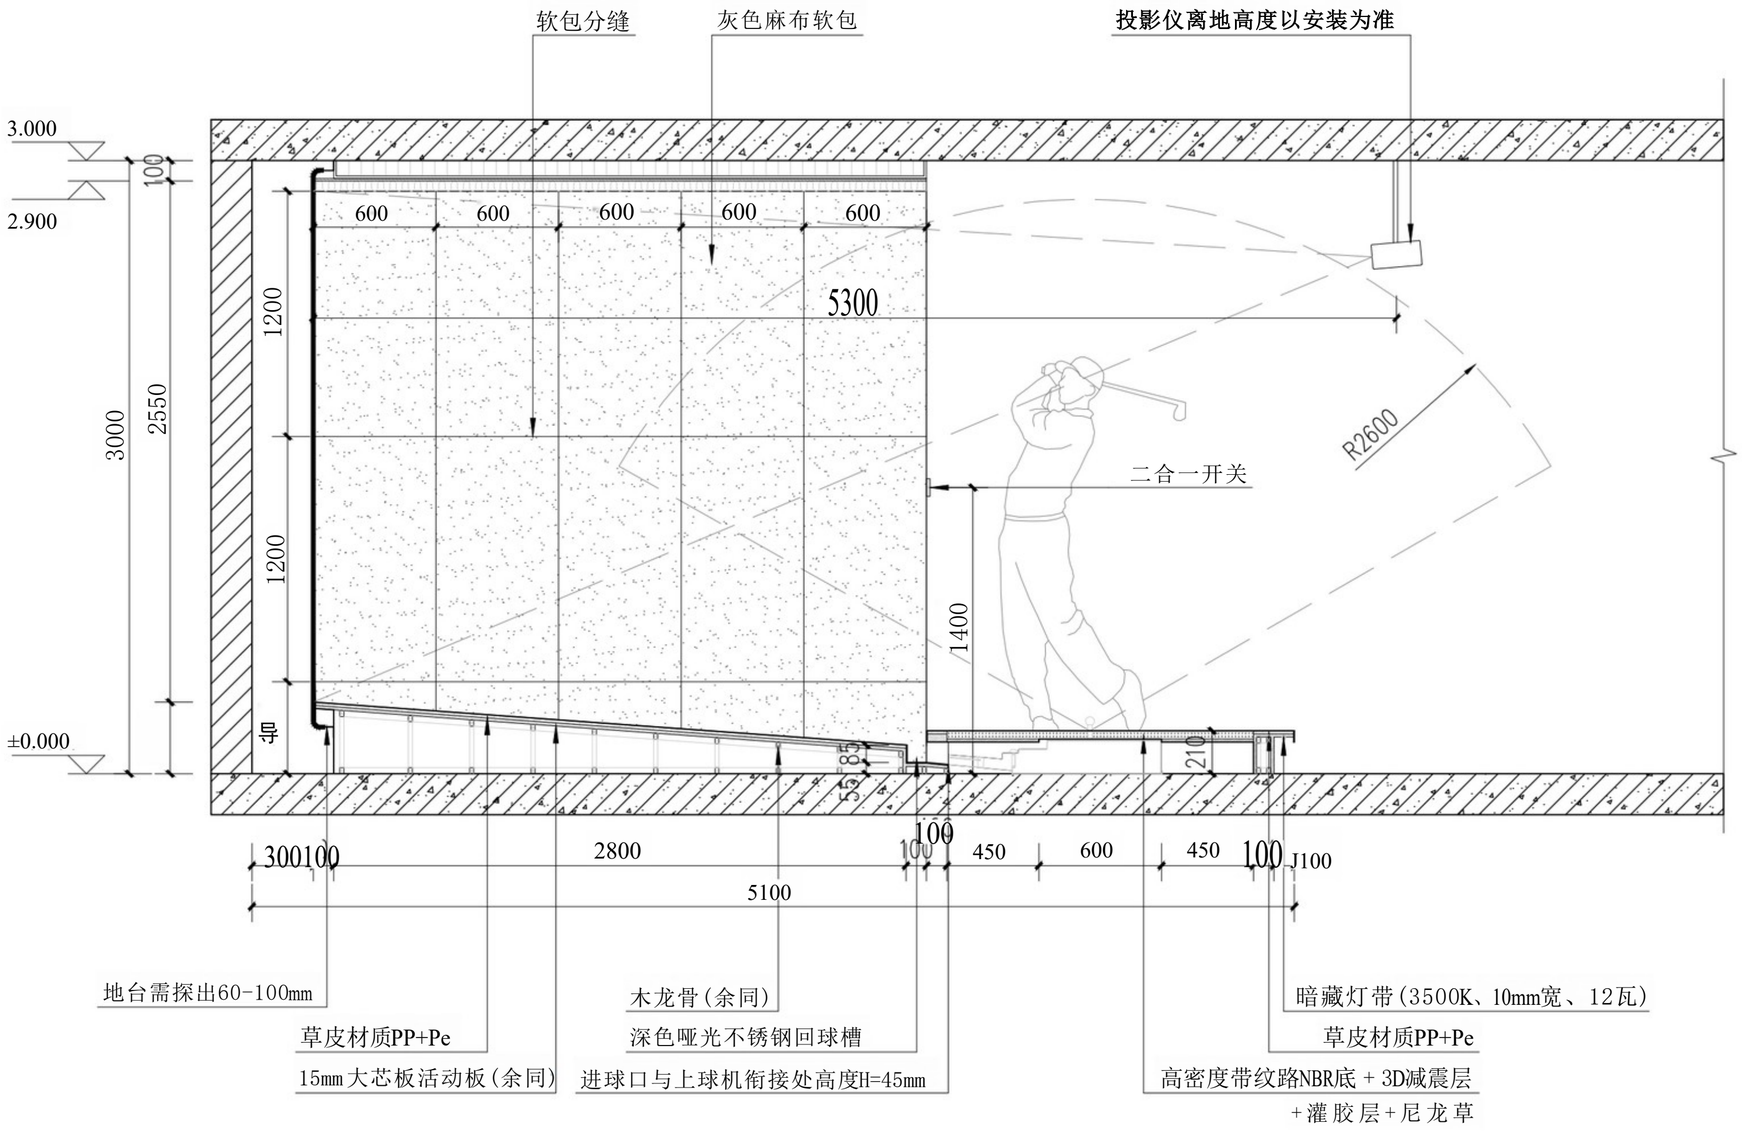

A-A 剖面图 1:30

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图 名

设备型号.

制图.

SCALE.
比例 1:30

DATE.
日 期 2026.2.


版权所有
施工时须以标注尺寸为准
施工单位须现场核查尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
年 R 为，最尺寸招在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图 幅：A2

SHEET NO. 图号

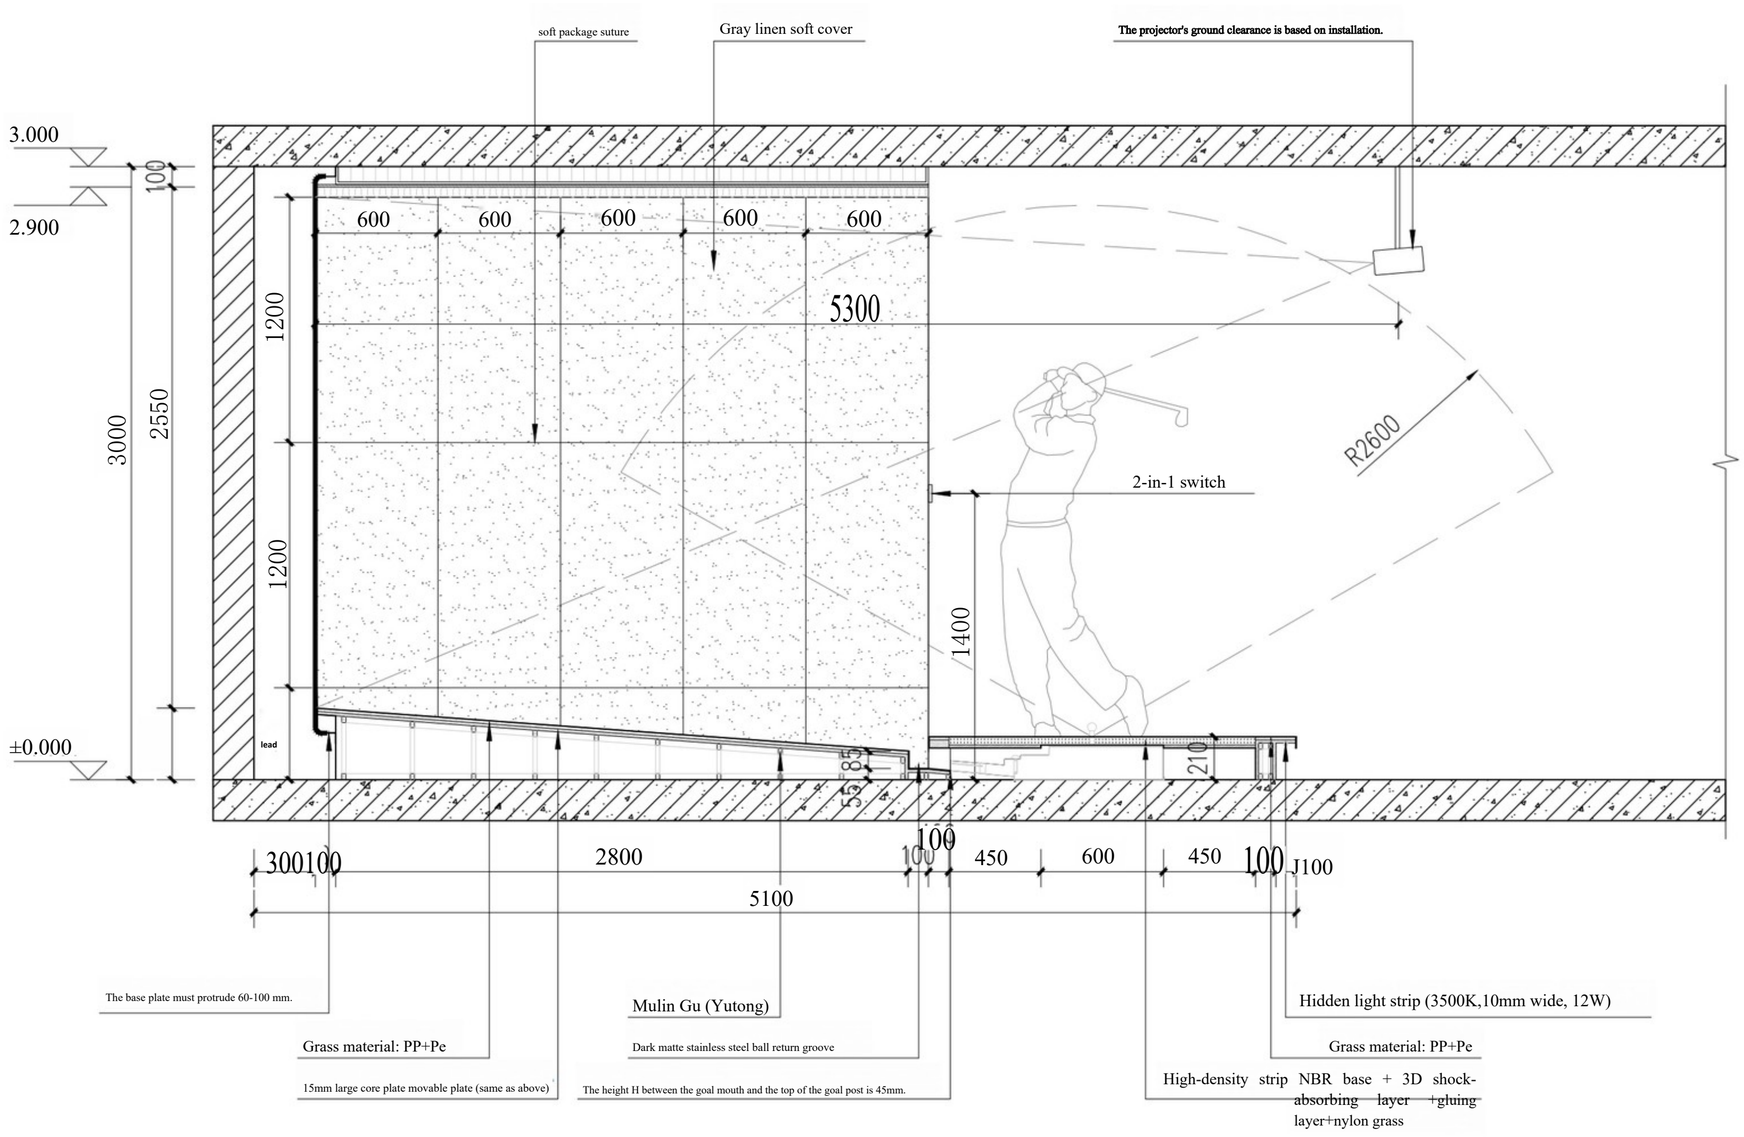

A-A Sectional view

1:30

CLIENT. Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图 名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date . 2026.2


all right reserved
The marked dimensions shall be taken as the standard
施工单位须现场校验尺寸
如有不符请立即通知设计单位
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
The annual R value is the maximum size recruitment.
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Figure size: A2

Sheet No.

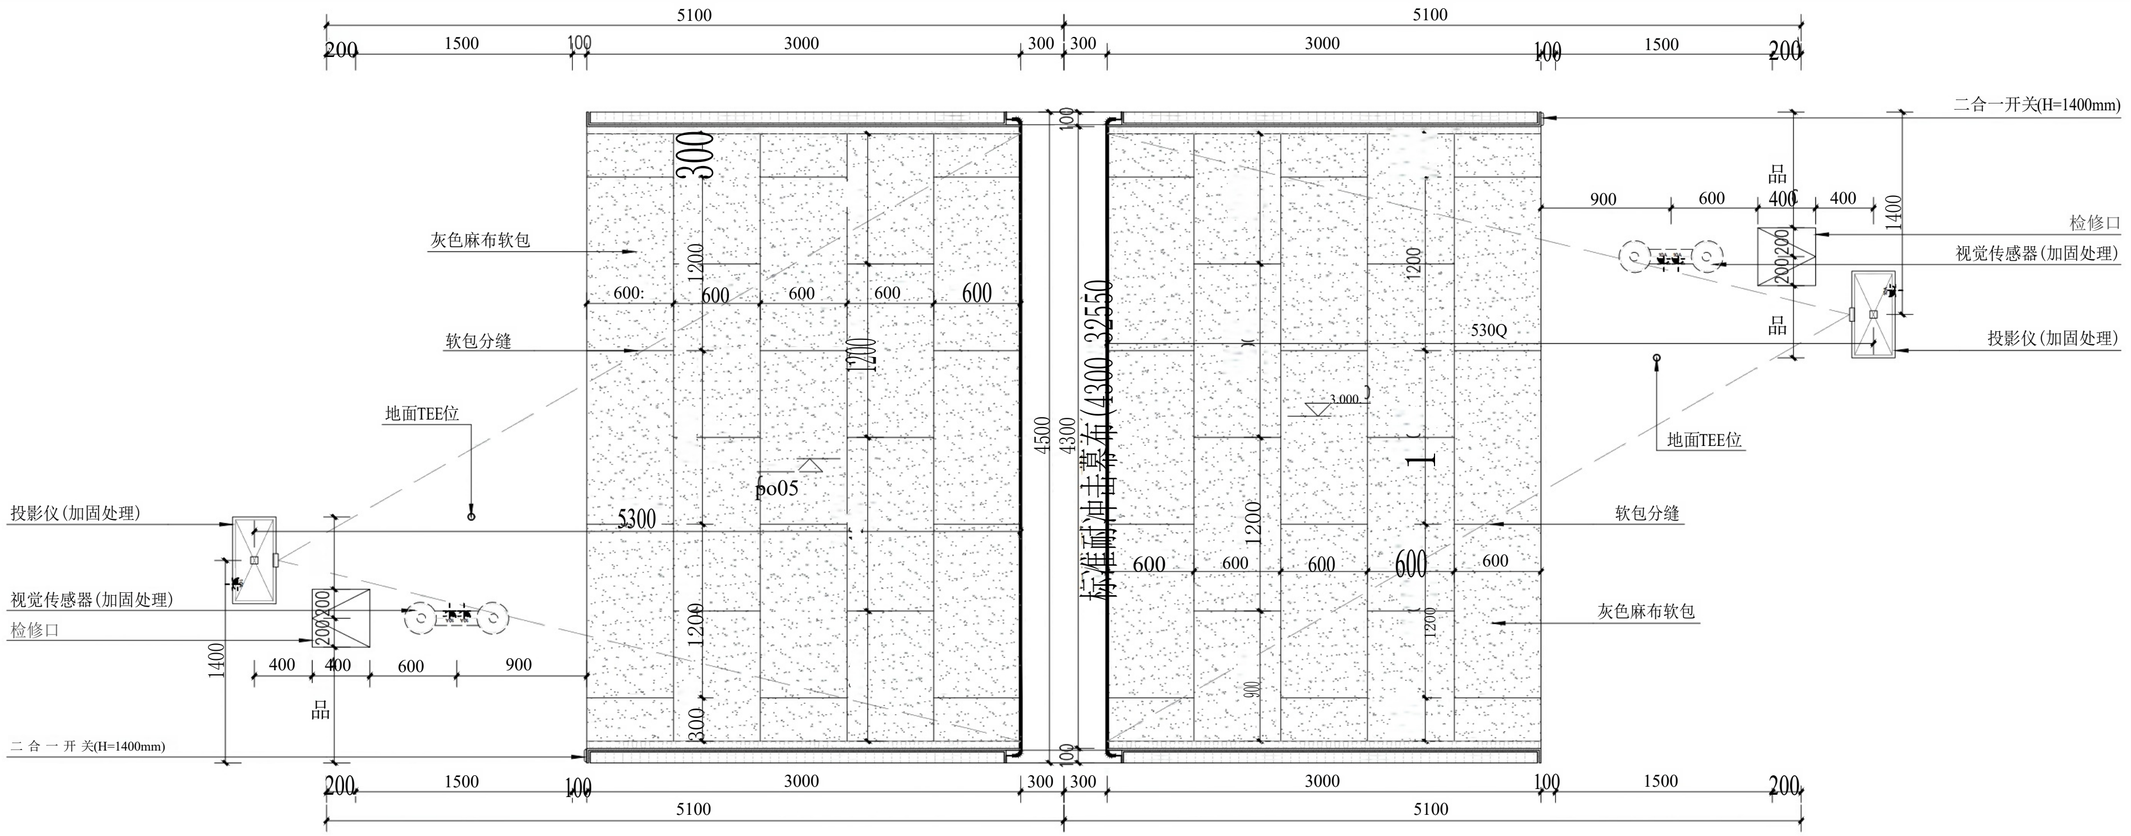

天花布置图1:30

注：图例仅为示意，实物请参见灯具选型表。

灯具图例说明

图例	名称	要求	安装高度	功率	色温	开孔尺寸	颜色
	TEE位射灯	装修预留电源	与天花吊顶高度一致	10W	4000K	110mm	白色
	视觉传感器	装修预留插座	与天花吊顶高度一致	150W		220mm	
	检修口		与天花吊顶高度一致			400*400mm	
	投影仪	装修预留插座	以投影仪公司安装为准				
	暗藏灯条	装修预留电源					

注：1.甲方安装休息区等区域照明必须为直流无频闪。
2.消防/烟感/音响及其他照明灯具部分由其他专业负责，空调及风口尺寸由专业厂家设计出图，空调出风均含带新风，灯位开孔尺寸以实际购买灯具为准。
3.所有电源插座必须接真实有效的地线。
4.所有电源/插座/开关/气管/数据线/信号线等线路全部套线管，布暗线，强电弱电必须分开套管。必须保持检修口上方的畅通，天花软包部分不能有消防喷淋。空调风口，休息区传感器高度不小于3.1m，具体尺寸根据现场而定。

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名


设备型号.

制图.
SCALE.
比例 1:30
DATE.
日期 2026.2

版权所有
施工时请以标注尺寸为准
如有不符须立即通知设计单位
This drawing is copyright
Contractor must check all dimensions on site
Contractor must be reported immediately to architects

备注:Notes
1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，，只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2
SHEET NO. 图号

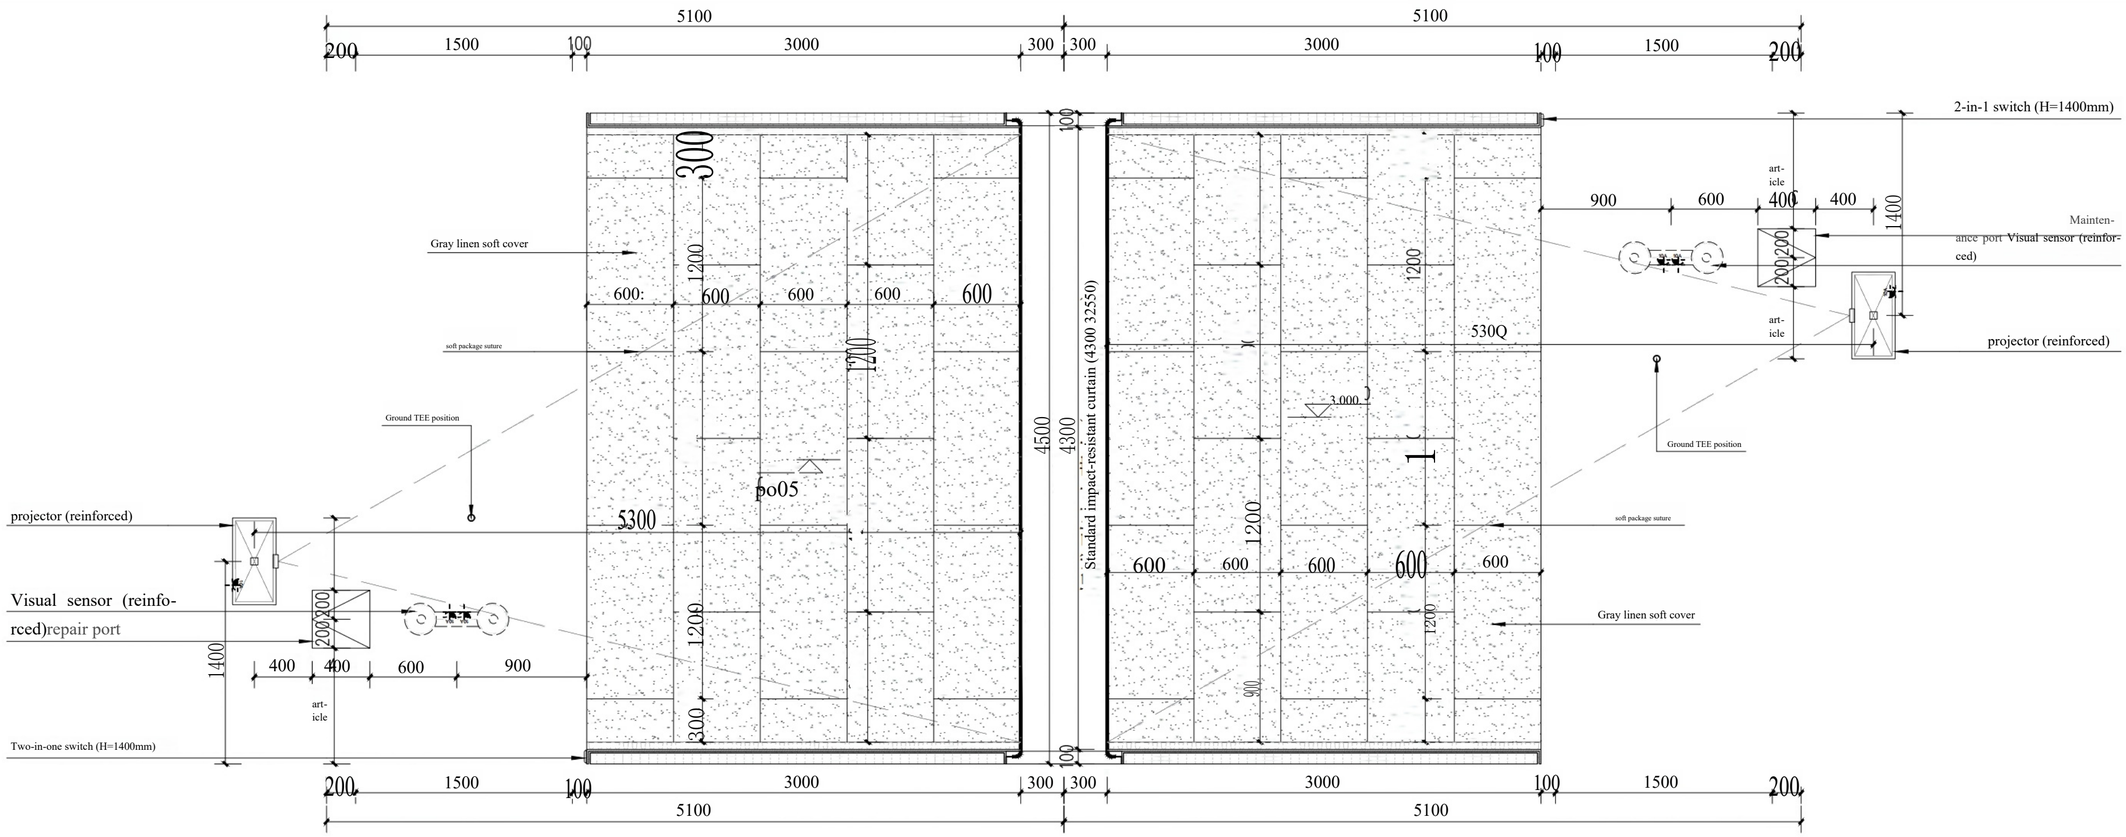

Plastering Layout Figure 1: 30

Note: The legend is for illustration only. Refer to the Lamp Selection Table for actual products.

Lamp Legend

Key	Name	Ask	Mounting height	Power	Colour temperature	Opening size	Pigment
	TEE headlight	Reserve power for renovation	Aligned with the ceiling height of the ceiling	10W	4000K	110mm	White
	Vision sensor	Reserve socket for renovation	Aligned with the ceiling height of the ceiling	150W		220mm	
	Access hole		Aligned with the ceiling height of the ceiling			400*400mm	
	Projector	Reserve socket for renovation	Installation shall be based on the projector manufacturer's specifications.				
	Hidden light strip	Reserve power for renovation					

Note: 1. The lighting in areas such as the Party A installation rest area must be DC without flicker.

2. Fire protection, smoke detectors, audio systems, and other lighting fixtures are managed by specialized departments. Air conditioning units and air outlet dimensions are designed by professional manufacturers, with all air outlets incorporating fresh air supply. The size of lamp openings is determined by the actual fixtures purchased.

3. All power sockets must be connected to a reliable and functional ground wire.

4. All power lines, sockets, switches, conduits, data cables, and signal lines must be installed in dedicated conduits with concealed wiring, ensuring separate conduits for high-voltage and low-voltage circuits. Maintenance access points must remain unobstructed, and ceiling soft packaging areas must not accommodate fire sprinklers. For air conditioning vents and rest area sensors, the minimum height should be 3.1m,with specific dimensions determined on-site.

CLIENT. Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图名

unit type .

Mapping.

SCALE.

Propo-rtion 1:30

DATE.

Date 2026.2

all right reserved

施工单位须提供此图尺寸

If any discrepancies are found, the design unit shall be notified immediately.

This drawing is copyright

D City h wokmedan1bo

Contractors must check all dimensions on site

Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。

2.本图纸应与说明，工地状况，建筑结构设计图及有关图

纸

need


Only for the maximum size according to

4.除特别注明外，图中所有尺寸均为毫米单位。

5.未签出图专用章，图纸无效。

Image size: A2

Sheet No.

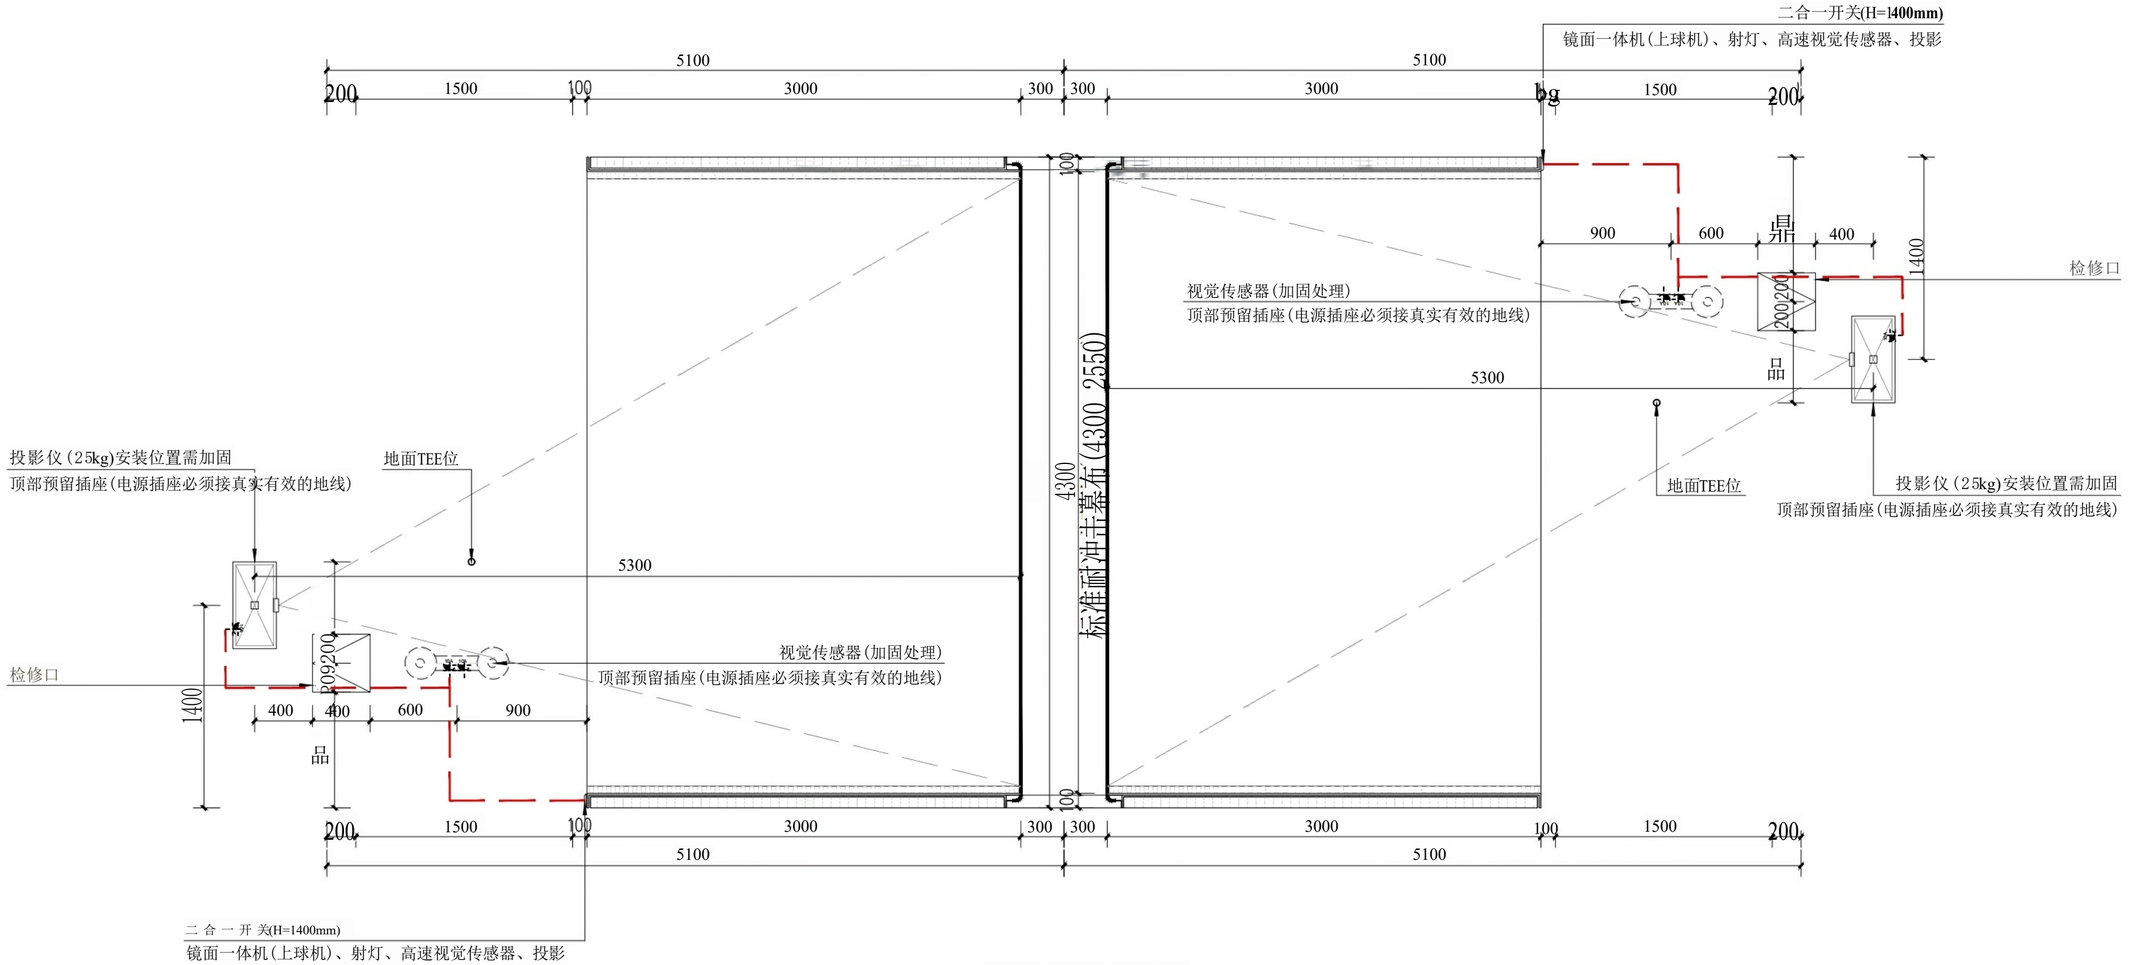

天花插座布置图130

注：强弱电各需穿50线管，间距300mm.

此强弱电仅为模拟器设备所用，不含其他强弱电。	
单	五孔插座(距离设备500之内)
-·—·-	暗藏灯条
一	暗装二合一开关面板H=1400mm



五孔插座示意图



射灯示意图

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2.


版权所有
地下时装仪标注尺寸为准
施工单位须现场核准尺寸
如有不符须立即通知设计单位
This drawing is copyright
D 市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，， 只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

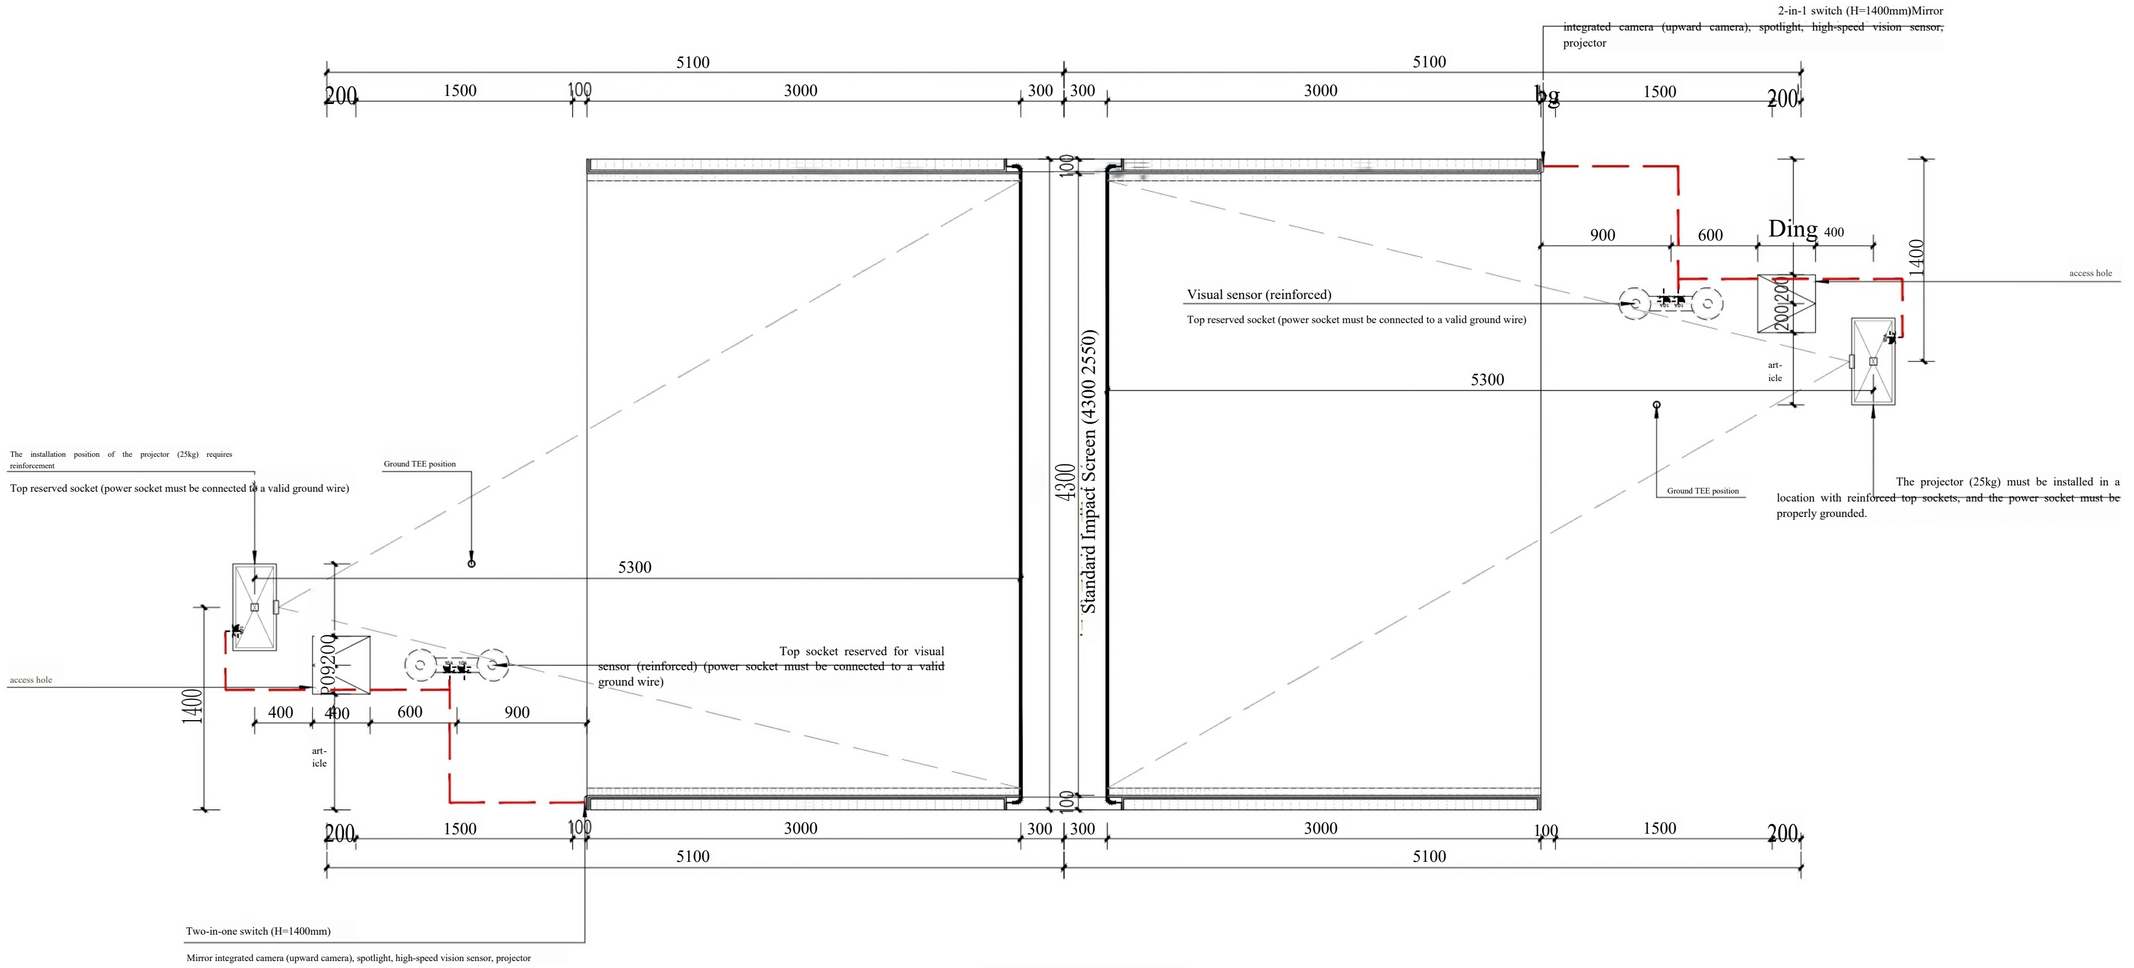

Slate Socket Layout 130

Note: Both high-voltage and low-voltage circuits require 50-gauge conduits spaced 300mm apart.

This power supply is exclusively for the simulator device and does not include other power supplies.	
Shan	Five-wire outlet (within 500 units of the device)
- • — • -	Hidden light strip
1	Hidden 2-in-1 switch panel, height 1400mm



Schematic diagram of five-hole socket



Spotlight diagram

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date 2026.2

all right reserved

If any discrepancies are found, the design unit shall be notified immediately.

This drawing is copyright

D City h wokmedan1bo

Contractors must check all dimensions on site


Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
3.
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A2

Sheet No.

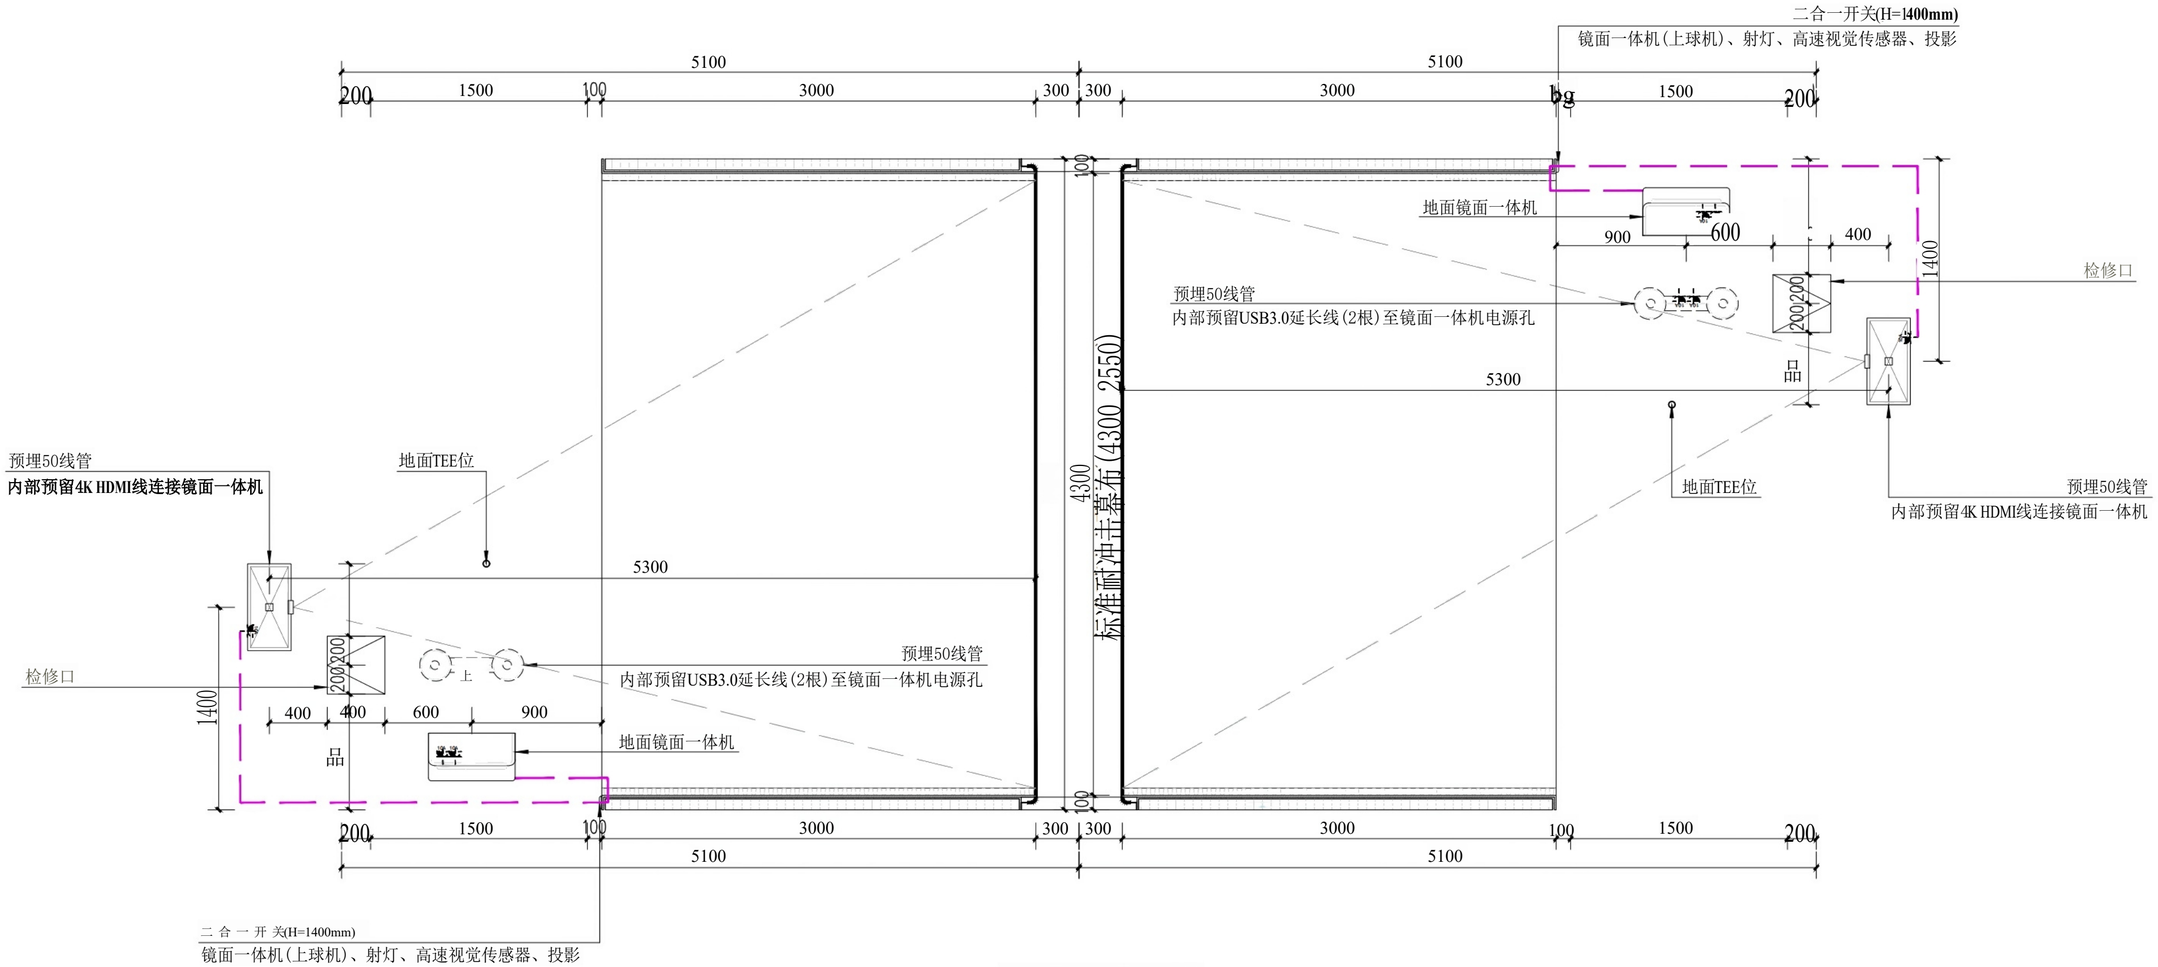

天花弱电布置图130

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2


版权所有
施工时须以标注尺寸为准
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，，只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

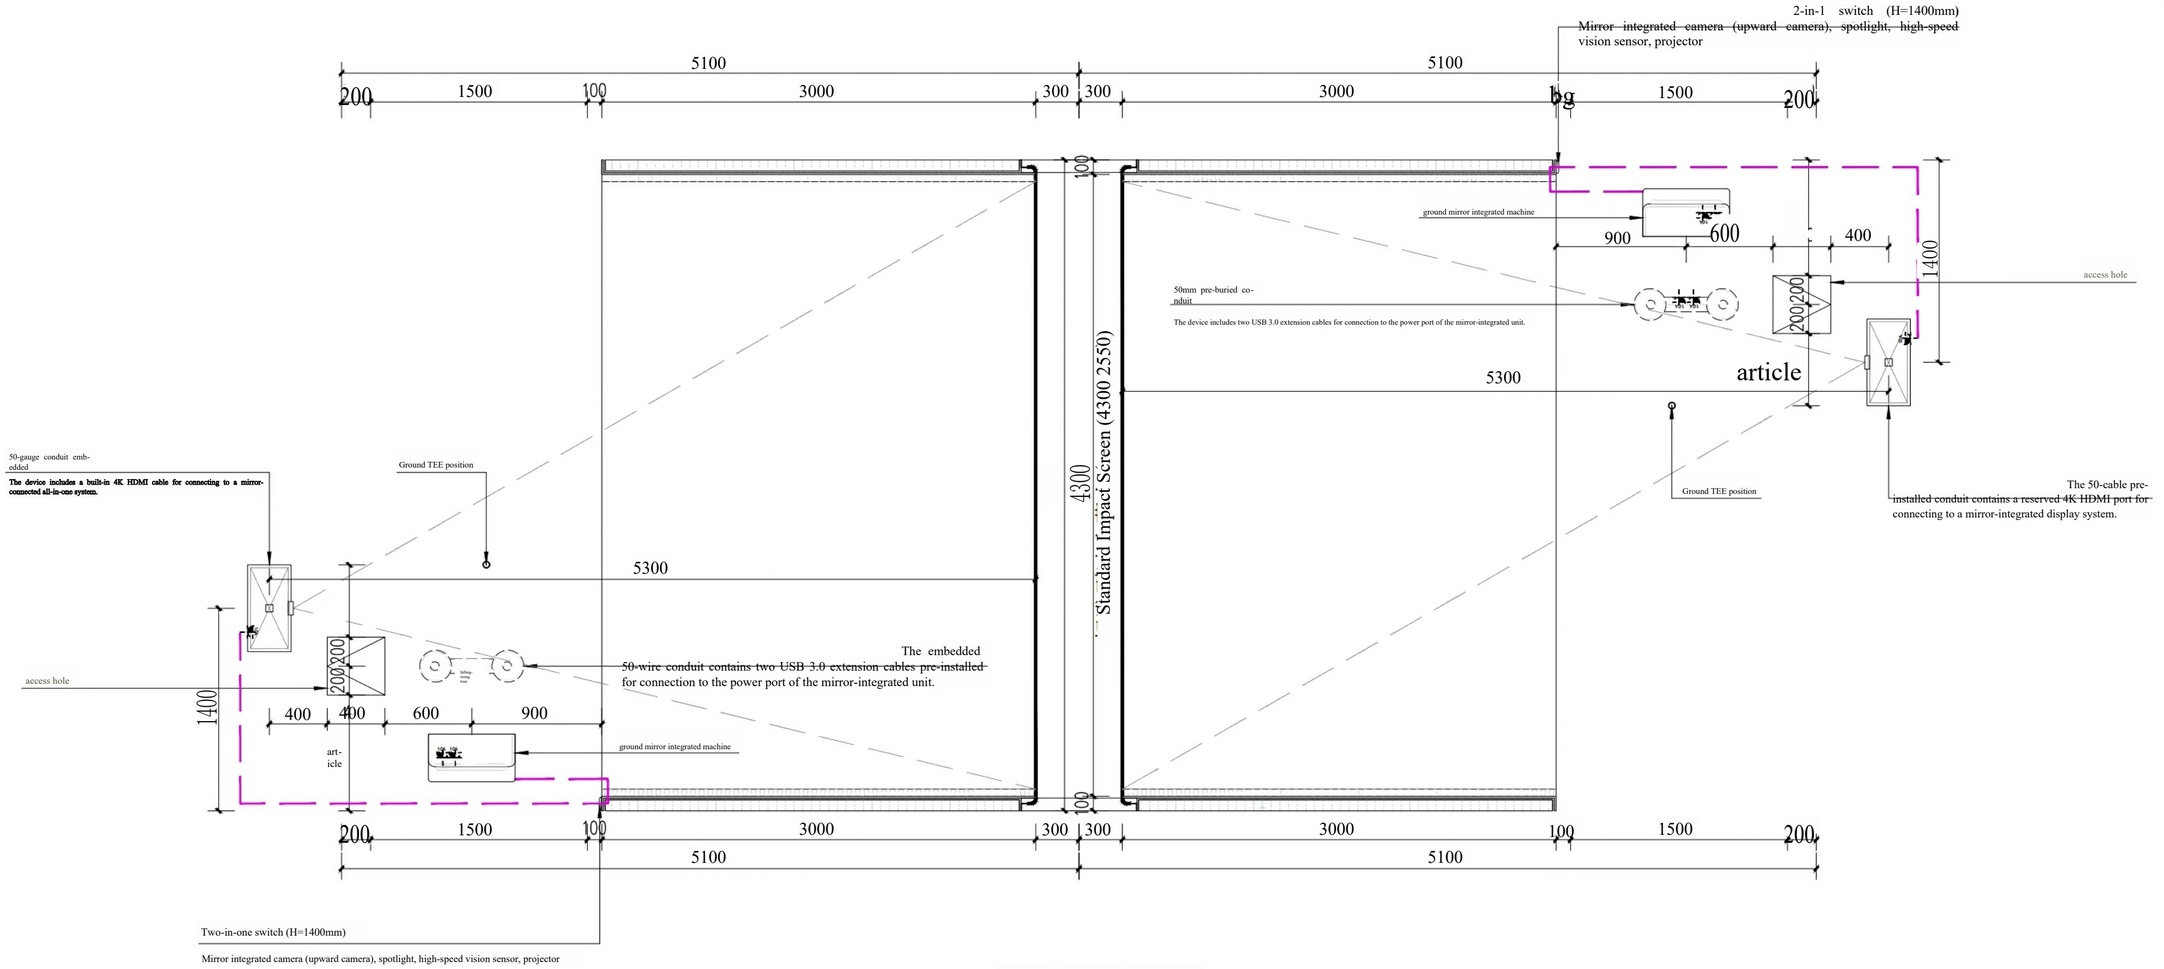

Tuberculosis Weak Current Layout Diagram 130

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图名

unit type .

Mapping.

SCALE:

Propo-rtion 1:30

DATE.

Date . 2026.2

all right reserved

The marked dimensions shall be taken as the standard during construction.

施工单位须现场校验尺寸

If any discrepancies are found, the design unit shall be notified immediately.

This drawing is copyright

D City h wokmedan1bo

Contractors must check all dimensions on site

Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。

2.本图纸应与说明，工地状况，建筑结构设计图及有关图

need


Only for the maximum size according to

4.除特别注明外，图中所有尺寸均为毫米单位。

5.未签出图专用章，图纸无效。

Image size: A2

Sheet No.

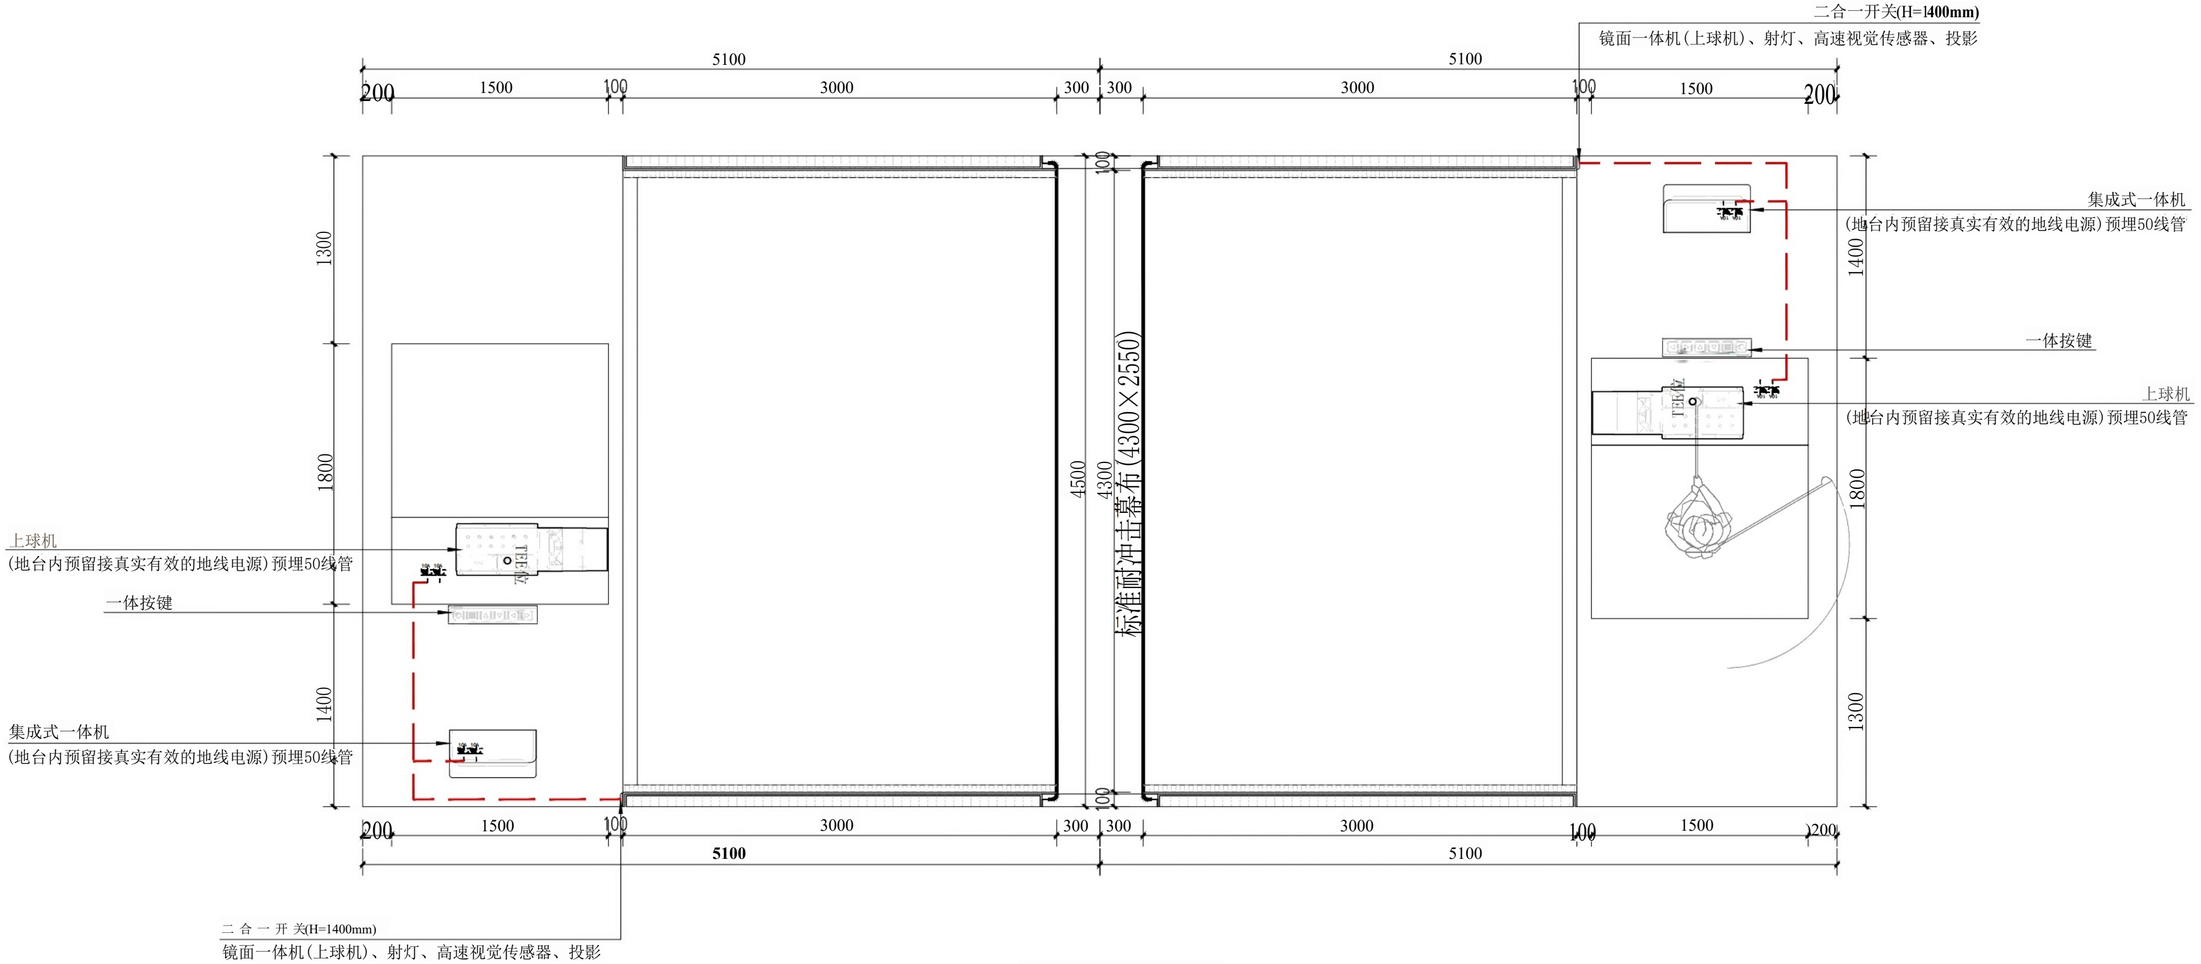

地面插座布置图130

注：强弱电各需穿50线管，间距300mm.

此强弱电仅为模拟器设备所用，不含其他强弱电。	
单	五孔插座(距离设备500之内)
-·—·-	暗藏灯条
一	暗装二合一开关面板H=1400mm



五孔插座示意图

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2.


版权所有
施工时须以标注尺寸为准
施工单位须现场校验尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported byroadsby to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
[illegible] 用 2, , 只与为，最尺寸据在
[illegible]
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

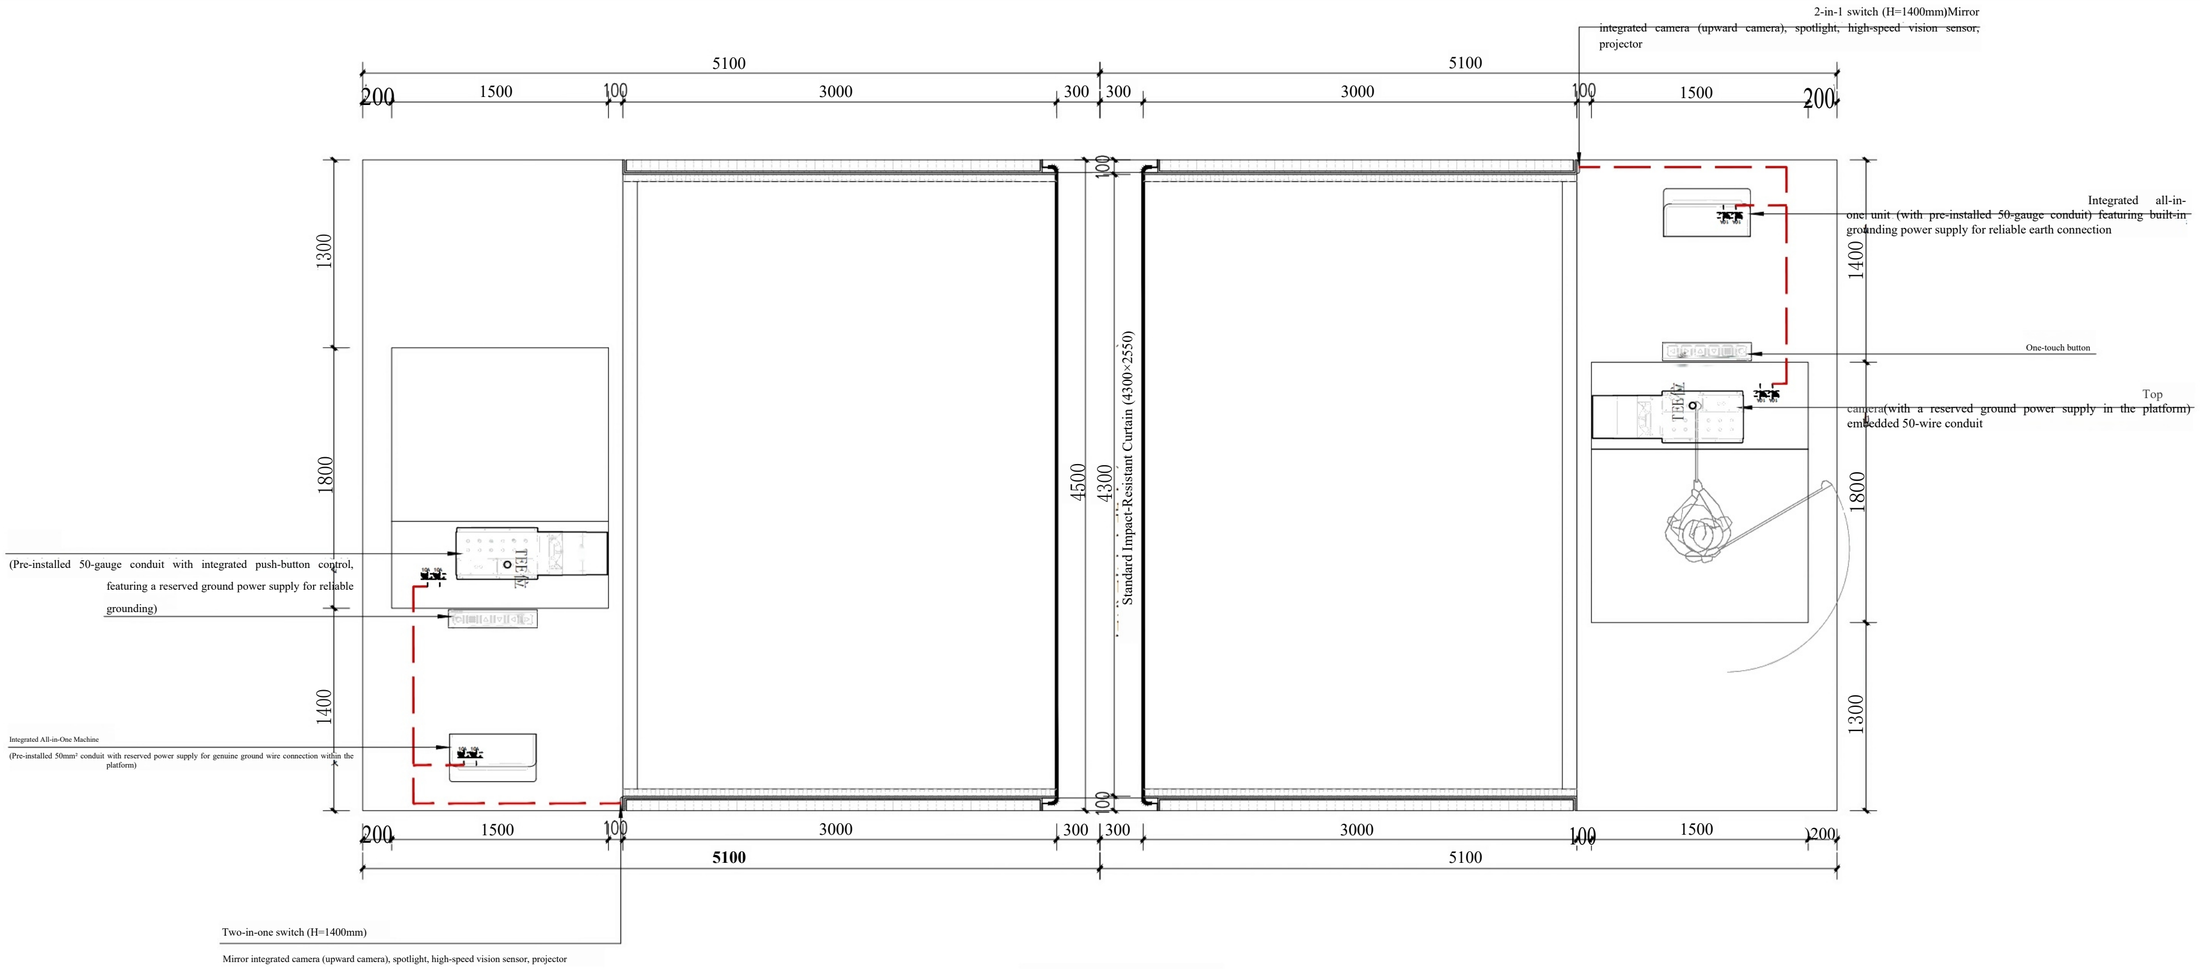

Floor socket layout diagram 130

Note: Both high-voltage and low-voltage circuits require 50-gauge conduits spaced 300mm apart.

This power supply is exclusively for the simulator device and does not include other power supplies.	
Shan	Five-wire outlet (within 500 units of the device)
– • — • –	Hidden light strip
1	Hidden 2-in-1 switch panel, height 1400mm



Schematic diagram of five-hole socket

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date . 2026.2.


all right reserved
All construction measurements shall be based on
the actual site dimensions. Any discrepancies must
be immediately reported to the design unit.
This drawing is copyright
D City h wokmedan1bo
Contractors must check all dimensions on site
Contractors must be reported hyrmediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
[illegible]
need
Only for the maximum size according to
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A2

Sheet No.

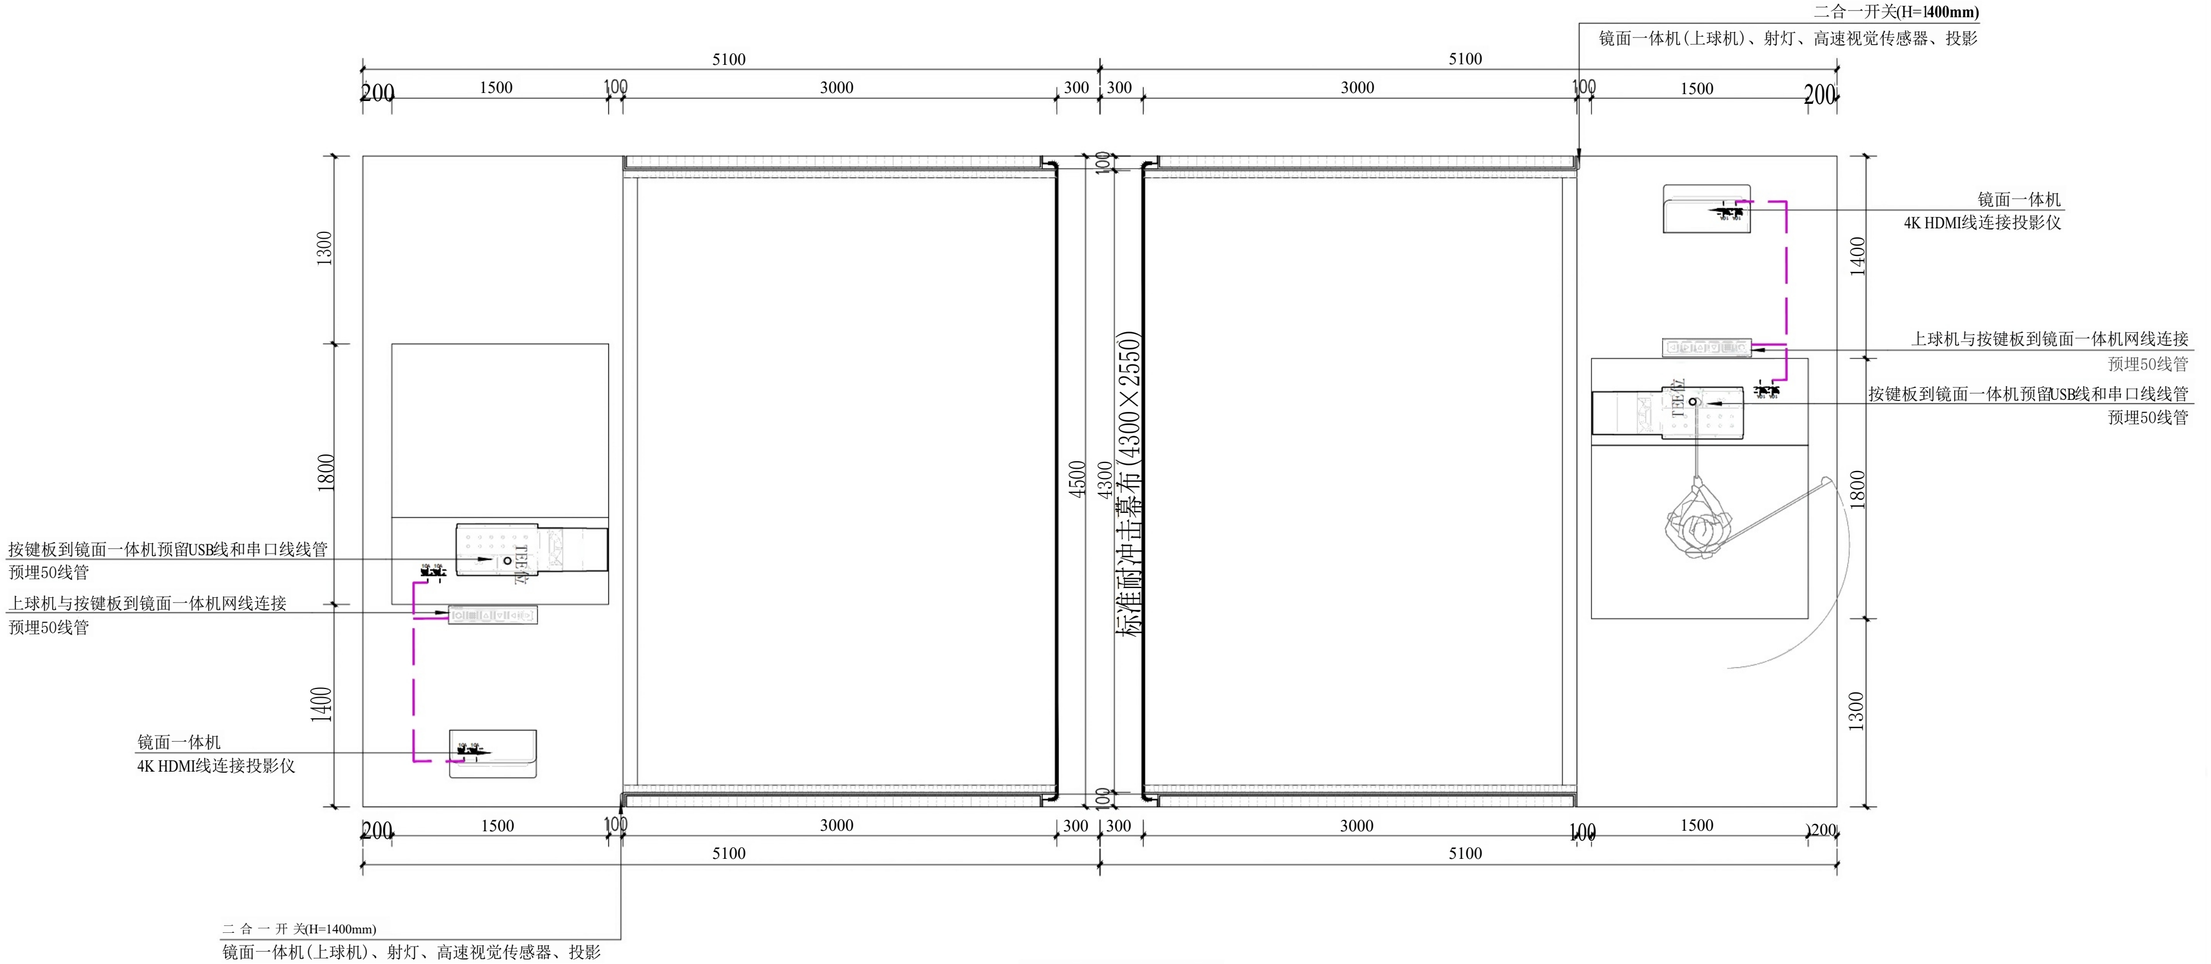

地面弱电布置图130

CLIENT建设单位

PROJECT TITLE. 项目名称

DRAWING TITLE. 图名

设备型号.

制图.

SCALE.

比例 1:30

DATE.

日期 2026.2.


版权所有
地下时请以标注尺寸为准
施工前应核对现场尺寸
如有不符须立即通知设计单位
This drawing is copyright
D市 h wokmedanlbo
Contractors must check all dimensions on site
Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
用，， 只与为，最尺寸据在
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

图幅：A2

SHEET NO. 图号

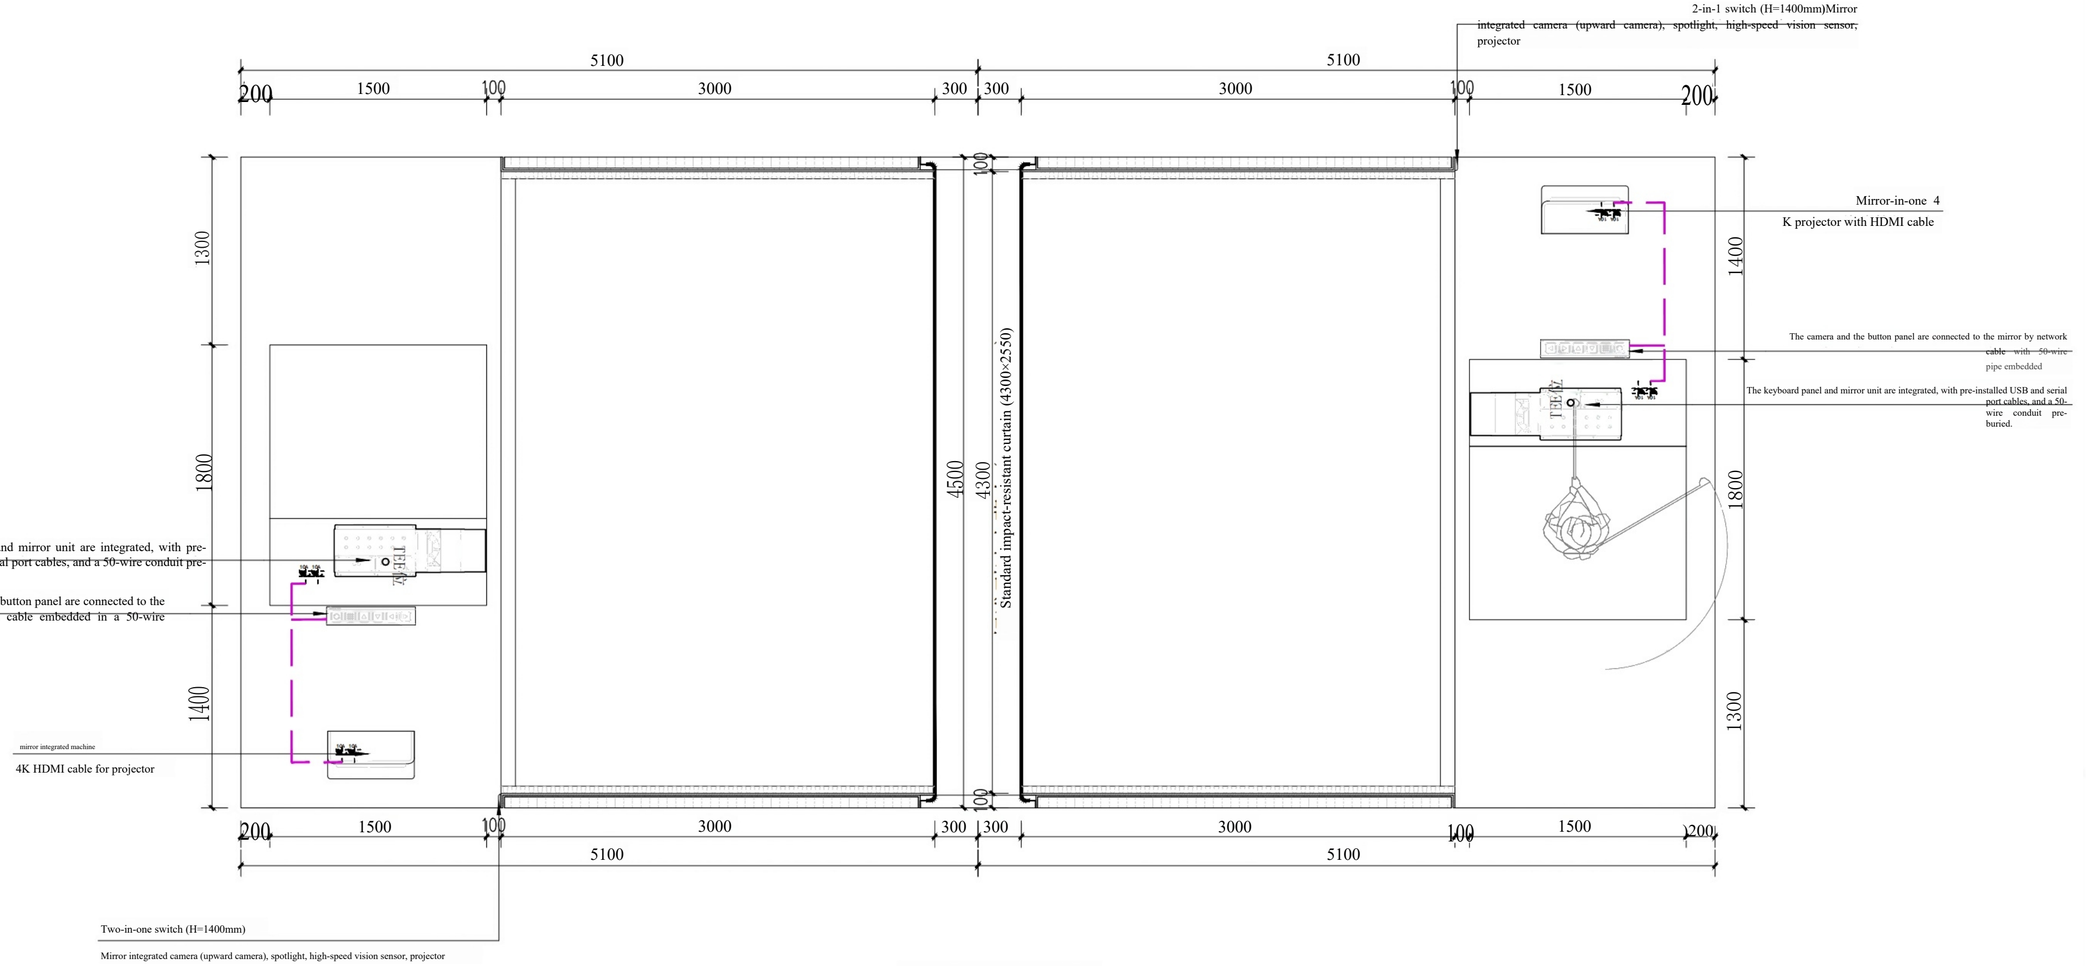

floor low voltage layout diagram

1:30

CLIENT.Construction Unit

PROJECT TITLE.Project Title

DRAWING TITLE. 图名

unit type .

charting .

SCALE.

scale 1:30

DATE.

date 2026.2

all right reserved

If any discrepancies are found, the design unit shall be notified immediately.

This drawing is copyright

D City h wokmedan1bo

Contractors must check all dimensions on site

Contractors must be reported immediately to architects

备注:Notes

1.本设计图纸版权归本公司所有，未经本公司书面同意，不得复印。
2.本图纸应与说明，工地状况，建筑结构设计图及有关图
3.
need Only for the maximum size according to
4.除特别注明外，图中所有尺寸均为毫米单位。
5.未签出图专用章，图纸无效。

Image size: A2

Sheet No.
